



**National Power Corporation**

**REQUEST FOR QUOTATION  
(NEGOTIATED PROCUREMENT – COMMUNITY PARTICIPATION 53.12)**

21 FEBRUARY 2023

\_\_\_\_\_  
\_\_\_\_\_  
Sir/Madam:

Please provide us with your best quotation for the items as specified in the Terms of Reference (TOR) for PR No. HO-UAR22-010, Ref. No. CMP221227-NA00449 (CMP3) and submit the same at the Bids and Contracts Services Division (BCSD), Ground Floor Diliman Quezon City on or before 09:30 A.M. of 06 MARCH 2023.

The documents to be submitted on the deadline of submission of quotations are indicated in the attached Terms of Reference ARTICLE 3 PRE-PROJECT START UP Item A. The Organized Social Groups shall submit the Legal, Technical and Financial Requirements.


In case no bid or insufficient number of bids is received on 06 MARCH 2023, the deadline for submission may be extended, as follows:

First (1<sup>st</sup>) Extension : \_\_\_\_\_  
Second (2<sup>nd</sup>) Extension : \_\_\_\_\_  
Third (3<sup>rd</sup>) Extension : \_\_\_\_\_

***The RFQ/Bid Proposal shall be submitted by the bidder to NPC via sealed offer.***

For further inquiries, please contact the BAC Secretariat, Ms. Nathalie Claire R. Abarquez at telephone no/s. 8921-3541/ local no. 5244 / Fax No. 8922-1622 with e-mail address at ncrabarquez@napocor.gov.ph and bcsd@napocor.gov.ph.

Very truly yours,

  
**RENE B. BARRUELA**

Vice President, Corporate Affairs Group and  
Chairman, Bids and Awards Committee



## TERMS OF REFERENCE (TOR)

### SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION

#### ARTICLE 1. OBJECTIVE

- To provide protection measures for the natural vegetation of the watershed as well as the vegetative rehabilitation projects, e.g., reforestation, agroforestry, Assisted Natural Regeneration (ANR), Bamboo Plantation, etc. against the destructive effects of forest fires in the watershed areas and in order to ensure the survival of the established plantation. The improved condition of the rehabilitated areas through the enhanced protection of the plantation will ensure the continuous and sustainable production of water to support the NPC power-generating plants for continuous operation, and also for environmental amelioration.

#### ARTICLE 2. COVERAGE

- Survey and mapping of fire line areas
- Staking and marking of fire line corners
- Clearing of weeds and shrubs of fire line areas
- Gathering and disposal of flammable debris

#### ARTICLE 3. PRE-PROJECT START UP

The Social Groups (CSG) shall submit the following:

##### A. For Organized CSG

##### 1. Legal Requirements

- a. Certificate of registration from the Department of Trade and Industry (DTI), Securities and Exchange Commission (SEC), Cooperatives Development Authority (CDA), Department of Agriculture (DA), Department of Labor and Employment (DOLE), National Commission on Indigenous People (NCIP); or in the case of the Civil Society Organizations, Non-Government Organizations or People' Organizations that are compliant with the requirements of a Community or Social Group (CSG), registrations from National Government Agencies (NGAs) or Local Government Agencies (LGUs); and
- b. A Sworn Affidavit (**Appendix "1"**) executed by the head or its authorized representative that affirms that:
  - i. None of its incorporators, officers or members is an agent or related by consanguinity or affinity up to the third (3<sup>rd</sup>) civil

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

degree to the HoPE, a member of the BAC, the Technical Working Group (TWG) or the Secretariat, or other official authorized to process and/or approve the proposal, contract, and release of funds; and

- ii. None of its incorporators, officers or members has a related business to the Community-based Project being procured at hand; or disclosure of the members if they have related business, if any, to the Community-based Project being procured at hand and the extent or percentage of ownership or interest therein.

**2. Technical Requirements**

- a. Statement of all its completed contracts similar to the Community-based Projects to be bid and/or list indicating the work experiences of their members similar to the Community-based Project to be bid **(Appendix "2")**

The End-user's acceptance or official receipt(s) or sales invoice issued for the completed contracts shall be attached to the statement as proof thereof.

***Financial Requirements***

- b. Photocopy or scanned copy of the bank book with complete bank account information; or a proof that it maintains books of accounts such a cash receipts journal, cash disbursement journal, general journal, and general ledger

For organized CSG that has participated in any government Community-based Projects for the past two (2) years:

- c. Latest Income Tax Return (ITR) for the preceding TAX Year or for new establishments, the most recent quarter's ITR or Business Tax Return; and.
- d. Updated Audited Financial Statement (AFS), which should not be earlier than two (2) years from the date of bid submission. The AFS should be stamped received by the BIR or accredited and authorized institutions, or electronically received via the AFS e-submission of the BIR with a filing reference number.

▪ **Posting and Submission of Request for Quotation**

- The End-user unit shall prepare the Request for Quotation (RFQ)
- BAC, shall post the RFQ for at least three (3) calendar days:
  1. on the website of the PE,
  2. in the premises of the PE

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

3. in at least three (3) conspicuous places where the Community-based Project shall be implemented (e.g., bulletin board, public transport terminals, public markets, etc.)
  4. In the Phillipine Government Electronic Procurement System (PhilGEPS) website
- The BAC shall also send the RFQs to CSGs of known qualifications thru the Upper Agno River Watershed Area Team (UARWAT)
  - Participating **CSGs shall submit their sealed quotation, if submitted manually**, or password-protected quotation, if submitted electronically, on the date and time prescribed in the terms and conditions of the RFQs, in accordance with Section 25.9 of the 2016 revised IRR of RA 9184.
  - The receipt of one (1) quotation is sufficient to proceed with the evaluation of the quotation. In the case there are no quotations received hours before the prescribed deadline, the BAC may extend the deadline for the submission of RFQ's three (3) times.  
Extensions of deadline shall likewise be posted for a period three (3) calendar days.

▪ **Opening and Evaluation**

- On the prescribed deadline, the BAC shall open submitted quotations and prepare an Abstract of Quotations setting forth the:
  - a. names of the CSGs that responded to the RFQ
  - b. corresponding price quotations; and
  - c. Lowest Calculated Quotation (LCQ) or Single Calculated Quotation (SCQ)
- The evaluation of the submitted quotations shall be completed within a maximum of seven (7) calendar days from the prescribed deadline.

▪ **Post-Qualification**

- The BAC shall exercise due diligence in validating the legal, technical, and financial capability of the CSG with LCQ or SCQ to supply and deliver the Goods, or to implement the Simple Infrastructure Project.
- If the BAC determines that the CSG with LCQ or SCQ passes the criteria for post-qualification, it shall declare the same as the Lowest Calculated and Responsive Quotation (LCRQ) or Single Calculated and Responsive Quotation (SCRQ).

In case of post-disqualification, the BAC shall notify the disqualified CSG and shall initiate and complete the conduct of the post-qualification with the next CSG with the second LCQ. If the next CSG, however, fails the

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

post-qualification, the procedure for post-qualification shall be repeated for the next CSG, and so on, until the LCRQ is determined for award of failure of bidding is declared.

- The post-qualification process shall be completed in not more than ten (10) calendar days from the receipt of notice to the CSG with the LCQ or SCQ, or in the case of the next CSG with the second LCQ, the post qualification shall be completed within a fresh period of 10 calendar days from the receipt of notice to the next CSG with the second LCQ. In exceptional cases, the HOPE may approve an extension of the post-qualification based on the BAC's recommendation, but in no case shall the aggregate period exceed twenty-five (25) calendar days from the determination of the LCQ.

- **Award of Contract**

- The BAC, after determining the legal, technical, and financial capability and the responsiveness of the quotation, shall recommend to the HoPE the award of contract in favor of the CSG with the SCRQ or LCRQ.
- Upon approval of the BAC recommendation, the HoPE shall issue a Notice of Award (NOA) within a period not exceeding ten (10) calendar days from receipt of BAC's recommendation and shall immediately enter into a contract with the CSG.

In case the CSG with the LCRQ or SRCQ fails, refuses, or is unable to enter into a contract with the PE, without justifiable cause, the HoPE of his duly authorized representative shall disqualify the CSG and direct the BAC to determine the responsiveness of the quotation of the next CSG with the second LCQ, or declare a failure of bidding and conduct a re-bidding with re-posting, if necessary, based on its determination, which shall be within seven (7) calendar days from the said declaration.

- The BAC, through its secretariat, shall post within three (3) calendar days from execution of the contract, the NOA, the contract, and the notice to proceed (NTP) in the
  1. website of the PE,
  2. in the premises of the PE
  3. in at least three (3) conspicuous places where the Community-based Project shall be implemented (e.g., bulletin board, public transport terminals, public markets, etc.)
  4. In the Phillipine Government Electronic Procurement System (PhilGEPS) website

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

▪ **Contract Implementation**

- Advance payment may be released in an amount not exceeding fifteen percent (15 %) of the total contract price in accordance with the Provisions of the Contract Implementation Guidelines for the Procurement of Goods, Supplies and Materials, and the Contract Implementation Guidelines for the Procurement of Infrastructure Projects, or Annexes "D" and "E" of the IRR of RA 9184.
- The PE shall require performance and warranty securities for the organized CSG, in accordance with section 39 and 62 of RA No. 9184 and its 2016 revised IRR.
- In case a different or new works are needed during project implementation, requests or proposals for any change or variation orders covering Simple Infrastructure Projects shall be made and evaluated in accordance with Contract Implementation Guidelines for the Procurement of Infrastructure Projects or "Annex E" of the 2016 revised IRR of RA 9184.
- The CSG, shall submit to the PE a statement of work accomplished or progress billing, and corresponding request for progress payment for work accomplished.
- Payment shall be released based on the terms provided in the contract and only upon validation by the End-User unit that the CSG has delivered or performed the outputs specified in the contract and the same has been inspected and accepted by the PE as satisfactorily in accordance with the technical specifications or scope of work, and applicable government budgeting, accounting, and auditing rules.
- In promoting financial inclusivity, the PE shall consider using to the extent possible authorized digital payment system in its financial transactions, subject to the applicable government budgeting, accounting, and auditing rules.

**ARTICLE 4. PROJECT START UP**

- Upon issuance by NPC and acknowledgement of Organized Community or Social Group of the Notice to Proceed, the latter shall be allowed a maximum of seven (7) calendar days to mobilize his/her group/workforce.
- The day one of first billing period, as stipulated in the Mode of Payments, shall be on the eight days after acknowledgement of Notice to Proceed. However, said day one of the first billing period may be adjusted earlier depending on the readiness of the Community or Social Group to start

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

the project, in which case, the Community or Social Group shall formally notify NPC of exact date of their day one.

- Before officially commencing work, the Community or Social Group shall seek first a clearance from the Chairman of the barangay where the project is located.

**ARTICLE 5. SCOPE OF WORK**

**Section 1. Surveying and Mapping**

- Fire lines shall be delineated and located along boundaries of plantation projects
- Fire line map with a scale of 1:10,000 shall be prepared
  - To be drawn and plotted on a tracing paper using the plantation maps as references/basis.
  - Natural boundaries such as ridges, creeks, gullies, and roadways may be used as fire lines.

**Section 2. Staking/ Marking of Corners**

- Prior clearing of the fire lines, corners must be staked/marked with two-by-two inches by five feet (2"x2"x5') wooden post with a height of one (1) meter and bamboo stick between corners at intervals of twenty-five (25) meters. Wooden post and bamboo stick shall be provided by the winning CSG.
- Minimum widths of fire lines shall be ten (10) meters and with variable length as specified in the project map.

**Section 3. Clearing of weeds and shrubs**

- Cut weeds and flammable debris in the fire line must be gathered and disposed of properly so as not to create a fire hazard zone. Tools to be used shall be provided by the winning CSG.

**Section 4. Gathering and disposal of flammable debris**

- Debris must be dispersed or control burning may be employed to dispose of the flammable debris in the fire line.
- If it warrants, cut vegetative matters may be disposed to be utilized as compost materials.

**ARTICLE 6. ACCOMPLISHMENT REPORTS AND DOCUMENTATION**

- The Community or Social Group shall submit an accomplishment report ("Annex C") based on the activities completed for every progress-billing.

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

- Progress report must be accompanied with geo-tagged pictures and shall be submitted regularly by the Community or Social Group for monitoring purposes.
- Reports and request for billing shall be signed by the Community or Social Group or his duly designated representative.
- The report shall contain information on how many laborers were utilized and the detailed accomplishment per day per activity. It may be also included significant experiences, problems encountered and recommendations for the improvement of the project implementation.
- The report shall be attached to the Request for Inspection and Notice of Billing hereto attached as “**Annex A**” and “**Annex B**”, respectively, for every completed activity per billing period.
- Final billing request shall have attached pictures taken before, during and after project completion. It should be taken in a single vantage point to show the development of the project.

**ARTICLE 7. SOURCE OF MANPOWER/WORKFORCE**

- The Community or Social Group's workforce in the conduct of these activities must comprise at least ninety (90 %) percent local community residents.
- The Community or Social Group must deploy a competent site Supervisor with experience in handling significant number of personnel in related projects.

**ARTICLE 8. WORK PLAN AND SCHEDULE**

- The Community or Social Group shall commence work within seven (7) working days from receipt of the Notice to Proceed.
- The schedule of implementation shall be in conjunction to the feasibility to undertake the work, e.g., fire line construction should be undertaken on the onset and until the end of the dry season.

ACTIVITY	CY 2023								
	M	M	M	M	M	M	M	M	M
	1	2	3	4	5	6	7	8	9
	(J)	(F)	(M)	(A)	(M)	(J)	(J)	(A)	(S)
1. Surveying and mapping									
2. Staking and marking of corners									
3. Clearing of weeds and shrubs									
4. Gathering and disposal of flammable debris									

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

**ARTICLE 9. PROJECT LOCATION AND CONTRACT DURATION**

- The projects were located in the three (3) Municipalities of Benguet within the Upper Agno River Watershed Area Team with a duration of ninety (90) days from the commencement of work. Completion of the work target prior to the ninety (90) days duration will be subject to inspection upon submission of request for inspection/evaluation. A certificate of acceptance from UARWAT will be issued once the accomplishment is found to be satisfactory.

<b>Location</b>	<b>Length</b>	<b>ABC Price</b>
1. Tojacap to Mt. Ambobongan, Kabayan, Benguet	4 LKM	128,071.67
2. Bacong to Mt. Ambobongan, Kabayan, Benguet	4 LKM	128,071.67
3. Bangao to Gusaran, Kabayan, Benguet	5 LKM	160,089.57
4. Hilltop-Mt. Patoktok-Dutac, Bokod, Benguet	5 LKM	160,089.57
5. Poblacion-Bagdan, Bokod, Benguet	3 LKM	96,053.74
6. Bangao – Kawal, Bokod, Benguet	4 LKM	128,071.67
7. Inidian to Damshack, Bokod, Benguet	4 LKM	128,071.67
8. Geweng to Adonot, Bokod, Benguet	4 LKM	128,071.67
9. Alam-am to Suggle, Atok and Bokod, Benguet	4 LKM	128,071.67
10. Comodian to Palew, Itogon, Benguet	4 LKM	128,071.67
11. Baloy to Camisong, Itogon, Benguet	4 LKM	128,071.67
12. Maro-oc to Saitan, Itogon, Benguet	4 LKM	128,071.67
13. Poblacion to Karao, Bokod, Benguet	4 LKM	128,071.67
<b>TOTAL</b>	<b>53 LKM</b>	<b>1,696,949.58</b>

**ARTICLE 10. MODE OF PAYMENTS**

- Payments shall be based on the progressive billing schemes and shall not exceed the allocated budget for the project. Sample billing is indicated in the table below.

<b>Payment No.</b>	<b>Nature of Payment</b>	<b>Basis/Indicator of Payment</b>	<b>Date Due/ Year</b>	<b>Total Cost Percentage</b>	<b>Total Amount/PhP</b>
<b>1</b>	1 <sup>st</sup> Billing Period (Mobilization Fee)	Inception Report/ Final Work Schedule	Month 1	15 % of the total amount (less 10 % retention fee)	<b>254,542.44</b>
<b>2</b>	2 <sup>nd</sup> Billing Period	Survey and mapping of fire line areas	Month 1	15 % of the total amount (less 10 % retention fee)	<b>254,542.44</b>

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

<b>3</b>	3rd Billing Period	-Staking/Marking of corners -Clearing of combustible materials - Gathering and disposal of flammable debris	Month 3	70 % of the total amount (less 10 % retention fee)	<b>1,187,864.70</b>
<b>4</b>	Release of Retention Fee	-Payment of 10 % retention Fee after inspection			
	<b>TOTAL</b>			<b>100 %</b>	<b>1,696,949.58</b>

**ARTICLE 11. PROCESSING OF PAYMENT**

- The inspection team shall be composed of the following:
  - Watershed Area Team (WAT)'s Senior Watershed Management Specialist.
  - Watershed Management Department (WMD) representative.
  - A representative from the LGU who will serve as witness during the inspection of completed activities.
  
- The Community or Social Group shall forward the following documents to the concerned WAT to warrant inspection of completed activity, to wit:
  - Request of Inspection.
  - Notice of Billing.
  - Certification that the laborers hired were already paid for the services rendered to be concurred by the laborers and noted by the Barangay Chairman; and
  - Pictures/photographs of before, during and after the activity.
  
- Upon receipt of the request for inspection and notice of billing, the WAT will coordinate with Plant representatives and convene the Inspection Team to cause an inspection within ten (10) working days.
- The Community or Social Group shall prepare two (2) sets of pictures of the completed activities as stated in the TOR (one set for payment purposes and the other set for file of the Area Team)
- The Community or Social Group shall be on site during the conduct of inspection and validation of completed activities.
- The Inspection Report may either recommend payment for the bill in such amount as may be warranted by actual accomplishments; or for its rejection, as the case may be.
- If the recommendation is for payment, the billing shall be immediately processed, and the payment shall be remitted to the Community or Social Group.

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

- If for rejection, the concerned WAT shall notify the Community or Social Group in writing within three (3) working days from Receipt of the Inspection Report of such fact and explaining the reasons thereof.
- NPC shall have the right to suspend payments on the contract, or impose such conditions as may be appropriate, if the results of the inspection indicate that accomplishments are below target as specified in the contract.

**ARTICLE 12. RETENTION FEE**

- To further guarantee accomplishment of the contracted services/project targets, an amount equivalent to ten percent (10%) of the total contract amount shall be retained by NPC as retention fee.
- Retention fee shall be disbursed to the Community or Social Group upon satisfactory completion of the contracted services/project targets.
- The ten percent (10%) retention fee shall be forfeited in favor of NPC if the requirements for satisfactory completion were not met.

**ARTICLE 13. SUBCONTRACTING/ASSIGNMENT**

- Subcontracting or assigning, wholly or in part, the services/project contracted stated on Article 3 (Scope of Work) of the Terms of Reference (TOR), is **prohibited**.
- Any subcontracting agreement or assignment entered into in violation of this condition shall be considered **null and void**. The Corporation shall not be answerable for any or all claims brought against the subcontractor, by its workers or by third parties.
- This prohibition does not cover the traditional practice of availing labor services, known as "pakyaw system" widely prevalent in the countryside.

**ARTICLE 14. PENALTY FOR DELAY**

- The contract consists of three (3) - billing period, which shall be completed as scheduled. Three (3) months is equivalent to Ninety (90) calendar days. All activities included in each billing period shall be accomplished on or before its expiration.
- The Community or Social Group shall be liable for **penalty** and agrees to pay the Corporation liquidated damages, in an amount equivalent to 1/10 of 1 % of the total value of the **unperformed services/uncompleted activities per billing period, for each calendar day of delay until** said activities included in that particular billing period is 100 % completed. For this purpose, it is clear that penalty is on a per billing period basis and **not** only after the ninety (90) days duration has elapsed.
- **Force majeure** shall refer to those events which could not be foreseen, or which though foreseen, were inevitable to make it impossible for the

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

Community or Social Group to carry out, in whole or in part, the obligations under the contract.

- Delays caused by ***force majeure*** are not covered by the penalty. The following are cases of ***force majeure***.
  - Those due to human causes such as civil wars, armed invasion, revolution, rebellion, insurgency, riots, strikes, armed blockades, civil disturbance/disobedience and other analogues causes; and
  - Those due to natural causes such as earthquakes, typhoons, storms, floods, prolonged drought, epidemics, and other similar phenomena.
- In case of ***force majeure***, the Community or Social Group shall notify the Corporation and the Watershed Area Team in writing, **within seven (7) days** after its occurrence, describing the same and its effects upon the performance of the contract.
- The Corporation shall, within **five (5) days** upon receipt of the notice, meet and decide on the most appropriate course of action to take under the circumstances, which may include **suspension of work or termination of the contract**.
- In case of suspension of work, the contract may be extended for a period equivalent to that for which the Community or Social Group was prevented from performing the work if climatic factors still warrant the performance of such work.
- In the event of termination, the Community or Social Group, upon receipt of the notice, shall take immediate steps to end the work in a prompt and orderly manner minimizing expenditures as far as practicable.
- The Corporation shall not be liable to the Community or Social Group except for work or services performed prior to the date of termination and for actual costs incurred in connection with the liquidation of work.
- The Community or Social Group shall turn over to the Corporation all records and documentation made as of the date termination.

**ARTICLE 15. OTHER LIABILITIES**

- The Community or Social Group shall be held liable and fully responsible to the safety and welfare of the "pakyaw" laborers contracted under this contract.
- In the event of minor accidents and/or more serious scenario such as fatal accidents, the Corporation shall not be held liable and is free from any financial obligations.

**ARTICLE 16. NON-COMPLIANCE**

- The Community or Social Group shall be held responsible for failure of the project because of negligence, non-satisfactory performance or abandonment. The Community or Social Group shall pay all costs, which may be attributed to the non-conformance, until such time the area is turned over to NPC. In this case, if climatic factor still permits, the contract shall be awarded to the next ranked eligible bidder following the

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

conditions stated in R. A 9184 or the "Government Procurement Reform Act".

**ARTICLE 17. PERFORMANCE SECURITY BOND**

- To guarantee the faithful performance of the Contract, the Community or Social Group shall post a performance security which is penal in nature and in and in accordance with the following:
  - Acceptance forms of the bond and corresponding amount (any or combination)
  - Cash-five percent (5 %) of the total contract price.
  - Managers or Cashier's Check – five percent (5 %) of the total contract price.
  - Irrevocable Standby Letter of Credit-five percent (5 %) of the total contract price. ISLOC issued and confirmed by Local Commercial Bank. These bank forms should be submitted to the jurisdiction of Philippine courts in the event a claim arises.
  - Bank Guarantee equivalent to ten percent (10 %) of the total Contract price.
  - Surety Bond issued by the Government Service Insurance System (GSIS)
    - o Thirty percent (30 %) of the Total contract price
    - o Surety Bond should contain the following conditions:
      - a. The bond is a penal bond and callable on demand.
      - b. The entire amount of the bond shall be forfeited in favour of the obligee upon default of the contractor.
      - c. In case of claim, the surety shall pay such claim within sixty (60) days from receipt by the Surety of the Obligee's notice of claim/demand letter notwithstanding any objection thereto by the principal, provided that the default of the principal is established by evidence of the Obligee.
- It is hereby also agreed that there be any amount due and payable to the Principal under the Contract guaranteed by this bond after the claim against a bond has been fully paid by the Surety, the Principal hereby assigns the same or sufficient amount thereof as collateral for the bond which the Obligee shall withhold and retain to be remitted/paid to the Surety upon demand to answer for the principal's liabilities to the Surety there under.
- It shall remain in full force and effect until completion of the scope of work and all the accomplishments are accepted by the obligee.

**CSGs LETTERHEAD WITH LOGO**

(Date)

**Mr. EMMANUEL A. UMALI**  
Manager  
Watershed Management Department

**THRU: BENJAMIN T. KIMMAYONG**  
Section Chief, UARWAT

**REQUEST FOR INSPECTION**

We are pleased to inform you that the required activities under Billing Period No. \_\_\_\_ had been 100 % completed, to wit:

- Activity No. 1: Survey and mapping of the 53 LKM fire line areas
- Activity No. 2: Staking and marking of corners
- Activity No. 3: Clearing of weeds and shrubs of fire line areas
- Activity No. 4: Gathering and disposal of flammable debris

In this regard, may we earnestly request the Inspection Team to conduct inspection and validation of the above-completed activities to warrant the corresponding payment indicated in the notice of billing.

Thank you.

---

Contractor  
(Signature over Printed name)  
Designation

cc. Benjamin T. Kimmayong  
Section Chief  
Upper Agno River Watershed Area Team

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

**"ANNEX B"**

**CSGs LETTERHEAD WITH LOGO**

(Date)

**Mr. EMMANUEL A. UMALI**  
 Manager  
 Watershed Management Department

**THRU: BENJAMIN T. KIMMAYONG**  
 Section Chief, UARWAT

**NOTICE OF BILLING PERIOD**

This is to bill the Upper Agno River Watershed Area Team-Watershed Management Department- National Power Corporation the total amount of \_\_\_\_\_ (\_\_\_\_\_) for the payment of (1<sup>st</sup>/2<sup>nd</sup>/3<sup>rd</sup>) billing period for the services rendered under Contract No. \_\_\_\_\_ for the Supply of Labor and Materials for the Establishment of 53 LKM fire line at various Locations.

<b>Location</b>	<b>Length</b>	<b>Bill Amount</b>
1. Tojacap to Mt. Ambobongan, Kabayan, Benguet	4 LKM	
2. Bacong to Mt. Ambobongan, Kabayan, Benguet	4 LKM	
3. Bangao to Gusaran, Kabayan, Benguet	5 LKM	
4. Hilltop-Mt. Patoktok-Dutac, Bokod, Benguet	5 LKM	
5. Poblacion-Bagdan, Bokod, Benguet	3 LKM	
6. Bangao – Kawal, Bokod, Benguet	4 LKM	
7. Inidian to Damshack, Bokod, Benguet	4 LKM	
8. Geweng to Adonot, Bokod, Benguet	4 LKM	
9. Alam-am to Suggle, Atok and Bokod, Benguet	4 LKM	
10. Comodian to Palew, Itogon, Benguet	4 LKM	
11. Baloy to Camisong, Itogon, Benguet	4 LKM	
12. Maro-oc to Saitan, Itogon, Benguet	4 LKM	
13. Poblacion to Karao, Bokod, Benguet	4 LKM	
<b>TOTAL</b>	<b>53 LKM</b>	

Thank you very much.

\_\_\_\_\_  
 Contractor  
 (Signature over Printed name)  
 Designation

cc. Benjamin T. Kimmayong  
 Section Chief  
 Upper Agno River Watershed Area Team

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

**“ANNEX C”**

**CSGs LETTERHEAD WITH LOGO**

(Date)

**Mr. EMMANUEL A. UMALI**  
 Manager  
 Watershed Management Department

**THRU: BENJAMIN T. KIMMAYONG**  
 Section Chief, UARWAT

**ACCOMPLISHMENT REPORT**

A. Overall

<b>Billing No.</b>	<b>Activity</b>	<b>Unit of Measure</b>	<b>Target</b>	<b>Accomplishment</b>	<b>% Accomplished</b>
<b>1</b>	Mobilization fee				
<b>2</b>	Survey and mapping of fire line areas	LKM	53		
<b>3</b>	-Staking/Marking of corners -Clearing of combustibile materials - Gathering and disposal of flammable debris	LKM	53		
<b>4</b>	-Payment of 10 % retention Fee after inspection	LKM	53		

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

**B. Per site**

<b>Location</b>	<b>Length</b>	<b>Accom- plishment</b>	<b>% Accomplished</b>
1.Tojacap to Mt. Ambobongan, Kabayan, Benguet	4 LKM		
2. Bacong to Mt. Ambobongan, Kabayan, Benguet	4 LKM		
3. Bangao to Gusaran, Kabayan, Benguet	5 LKM		
4. Hilltop-Mt. Patoktok-Dutac, Bokod, Benguet	5 LKM		
5. Poblacion-Bagdan, Bokod, Benguet	3 LKM		
6. Bangao – Kawai, Bokod, Benguet	4 LKM		
7. Inidian to Damshack, Bokod, Benguet	4 LKM		
8. Geweng to Adonot, Bokod, Benguet	4 LKM		
9. Alam-am to Suggle, Atok and Bokod, Benguet	4 LKM		
10 Comodian to Palew, Itogon, Benguet	4 LKM		
11. Baloy to Camisong, Itogon, Benguet	4 LKM		
12. Maro-oc to Saitan, Itogon, Benguet	4 LKM		
13. Poblacion to Karao, Bokod, Benguet	4 LKM		
<b>TOTAL</b>	<b>53 LKM</b>		

For your information and reference.

Contractor  
(Signature over Printed name)  
Designation

cc. Benjamin T. Kimmayong  
Section Chief  
Upper Agno River Watershed Area Team

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

**Appendix "1"**

**REPUBLIC OF THE PHILIPPINES)  
CITY/MUNICIPALITY OF \_\_\_\_\_) S.S**

**AFFIDAVIT**

I, [ Name of Affiant], of legal age, [Civil Status], [Nationality], and residing at [Address of Affiant], after having been duly sworn in accordance with law, do hereby depose and state that:

1. I am the (Head/Authorized Representative) of (Name of Community or Social Group).
2. That the incorporators, organizers, officers or members of our organization are the following.

Name	Position

1. Upon consultation and communication with the above-named individuals, I confirm and certify that:
  - a. None of us is an agent of or related by consanguinity or affinity up to the third civil degree to the Head of the Procuring Entity, members of the Bids and Awards Committee, the Technical Working Group, or the BAC Secretariat, or other officials of (Name of Procuring Entity) authorized to process and/or approve the proposal, contract, and release of funds in favor of the Community or Social Group; and
  - b. [ Include this paragraph if all Organized Community or Social Group Officers and members do not have any related business to the Community-based Project being procured] None of us has any related business to the Community-based Projects being procured at hand.
  - c. [Include this paragraph if any of those identified Organized Community or Social Group Officers or members must disclose his/her related business, including the extent or percentage of his/her ownership or interest therein.] The following officers or members of our Organized Community or Social Group has/have related business to the Community-based Project being procured at hand, including the corresponding extent or percentage of ownership or interest therein:

Name	Name or Nature of Related Business	Extent or Percentage of Ownership or interest in the Related Business

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---

- d. Include this paragraph if no performance or warranty security is prescribed by the Procuring Entity for Unorganized Community or Social Groups] Considering that the posting of a performance security has been dispensed with, as determined by the Procuring Entity, I hereby commit that our Unorganized Community or Social Group shall perform and deliver all the obligations and undertakings under the contract covering the procurement at hand. I further agree and accept that our failure to perform or deliver any of such obligations and undertakings shall result in Blacklisting of our Community or Social Group for not more than two (2) years in all government procurement activities following the procedure under RA No. 9184, its revised IRR and associated issuances.
- e. In case advance payment was made or given, failure to perform or deliver any of the obligations and undertakings in the contract shall be sufficient grounds to constitute criminal liability for Swindling (Estafa) or the commission of fraud with unfaithfulness or abuse of confidence through misappropriating or converting any payment received by a person or entity under an obligation involving the duty to deliver certain goods or services, to the prejudice of the public and the government of the Philippines pursuant to Article 315 of Act No. 3815 s. 1930, as amended, or the Revised Penal Code.

IN WITNESS WHEREOF, I have hereunto set my hand this \_\_\_\_ day \_\_\_\_, 2022  
at \_\_\_\_\_, Philippines.

[Insert NAME OF COMMUNITY OR  
SOCIAL GROUP REPRESENTATIVE]  
[Insert signatory's legal capacity]  
Affiant

**[Jurat]**

[Format shall be based on the latest Rules on Notarial Practice]

**SUPPLY OF LABOR AND MATERIALS FOR THE ESTABLISHMENT OF 53 LKM FIRELINE AT VARIOUS LOCATIONS FOR UPPER AGNO RIVER WATERSHED (UNDER UC-EC PLAN 9) NEGOTIATED PROCUREMENT THROUGH COMMUNITY PARTICIPATION**

---



**Appendix "2"**

**STATEMENT OF COMMUNITY GROUP'S COMPLETED CONTRACTS SIMILAR TO THE COMMUNITY-BASED PROJECT TO BE BID OR LIST INDICATING THE WORK EXPERIENCES OF MEMBERS SIMILAR TO THE COMMUNITY-BASED PROJECT TO BE BID**

<b>Name of Completed Contract</b>	<b>Contract Date</b>	<b>Period/Duration/Delivery Date</b>	<b>Amount Involved</b>	<b>Definition or Description of the project or major categories of work</b>	<b>Supporting Documentary Proofs (e.g., User acceptance, Official Receipts, sales invoice) Attached as Annex " _ "</b>



TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	269006.85	1839348.36
2	270580.43	1840766.75

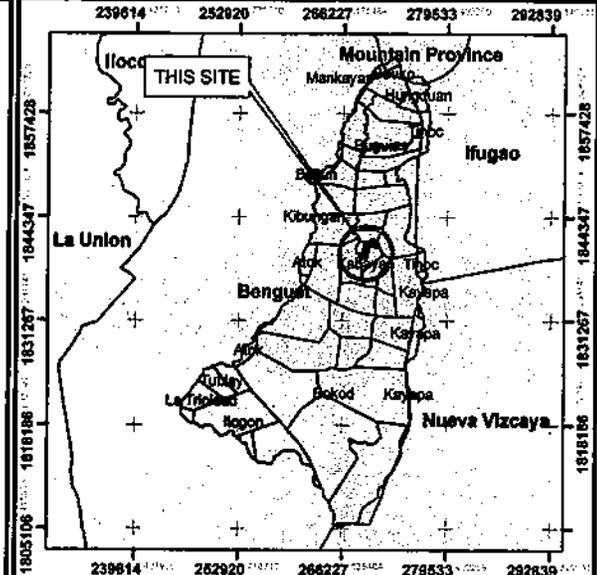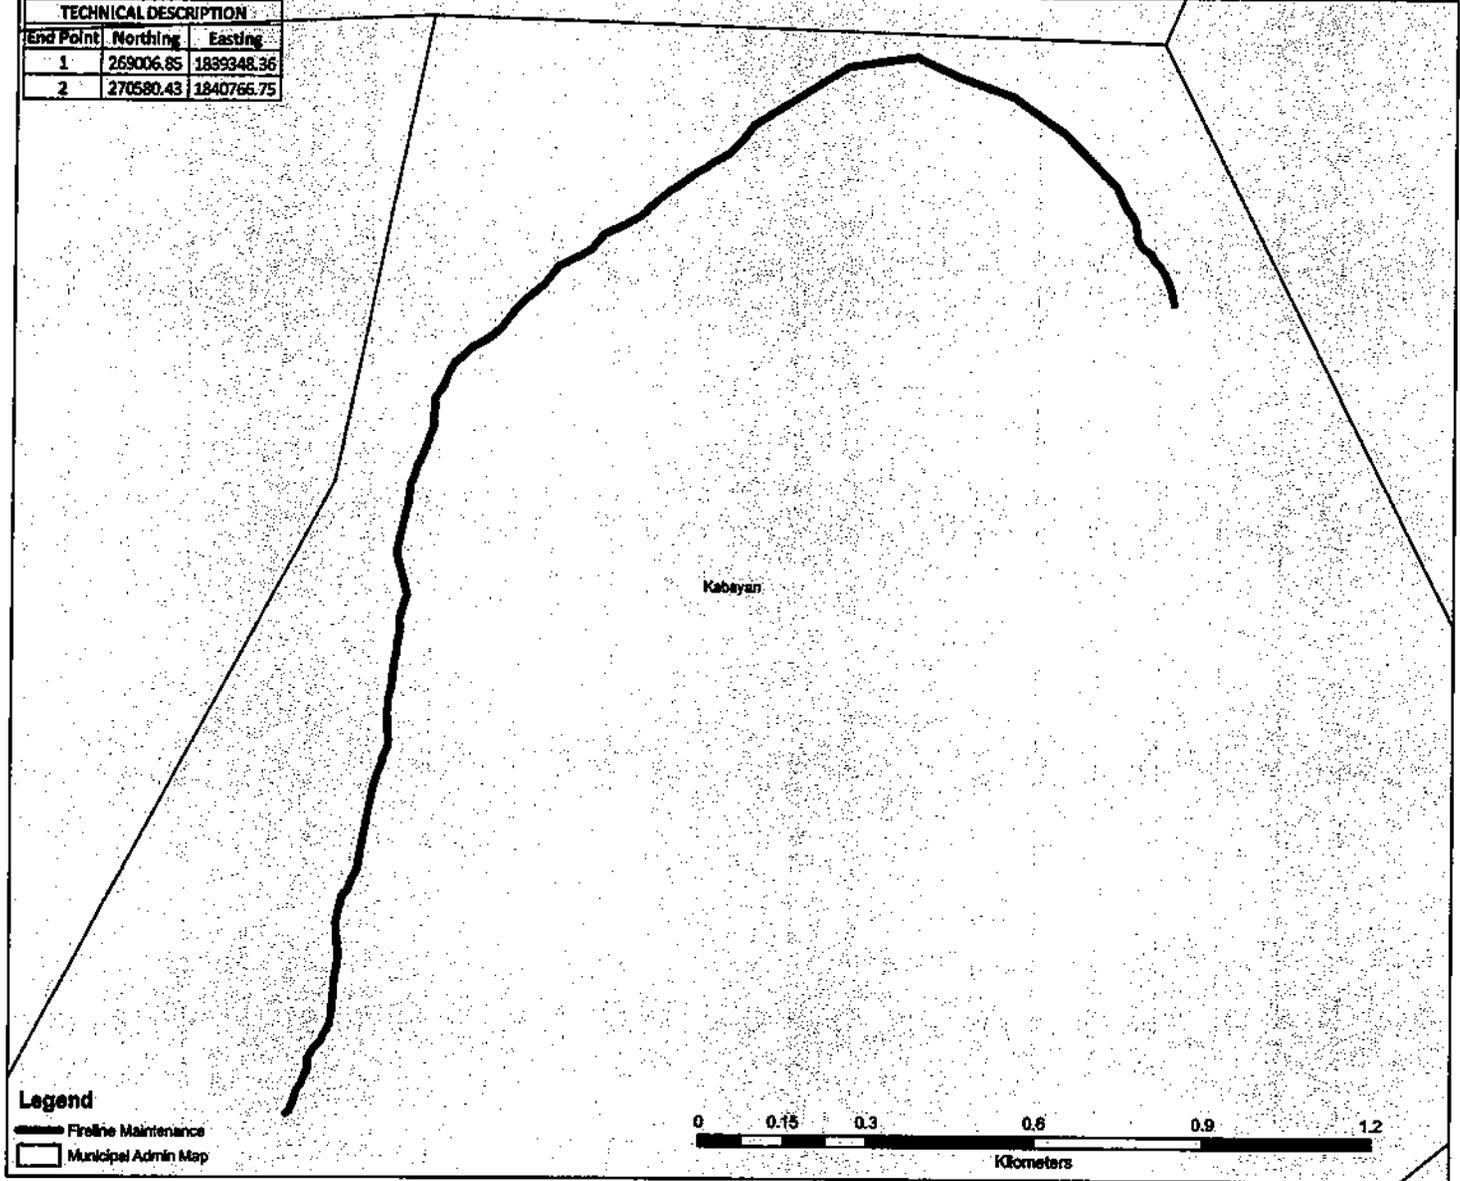

**LOCATION MAP**



Scale: 1:9,196  
 Map Projection:  
 Universal Traverse Mercator (UTM) Zone 51N  
 World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
 Upper Agno River Watershed Area Team  
 Watershed Management  
 National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: **BACONG TO MT. AMBOBONGAN**  
 MUN. / CITY OF: **KABAYAN**  
 PROVINCE OF: **BENGUET**  
 ISLAND OF: **LUZON**  
 CONTAINING AN AREA OF: **4 LKM**

**FINDINGS:**

1. VEGETATIVE COVER	<input type="checkbox"/> ADEQUATELY FORESTED	<input type="checkbox"/> INADEQUATELY STOCK
	<input type="checkbox"/> GRASSES/COGON	<input type="checkbox"/> BARED/DENUDED
2. TOPO SITUATION	<input type="checkbox"/> FLAT (0-18%)	<input type="checkbox"/> ROLLING (19-30%)
	<input type="checkbox"/> STEEP (>30%)	
3. OWNERSHIP	<input type="checkbox"/> CLAN/FAMILY	<input type="checkbox"/> ASSOCIATION
	<input type="checkbox"/> INDIVIDUAL	



4. REP/CONTROL POINTS	NO. _____
BUFFER MONUMENT	NO. _____
PUBLIC LAND	NO. _____
SUB-MONUMENT	NO. _____
CADASTRAL SURVEY	NO. _____
MONUMENT	NO. _____
JUNCTION	NO. _____
_____ ROADS	
_____ RIVERS	

**LAND-USE SURVEY MAPPING**

**PREPARED BY:**  
  
**MHERWIN S. CIPRIANO**  
 Wat. Mgmt. Officer

**NOTED BY:**  
  
**BENJAMIN T. KIMMAYONG**  
 Section Chief-UARWAT

TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	276138.3	1841227
2	271608.3	1843290

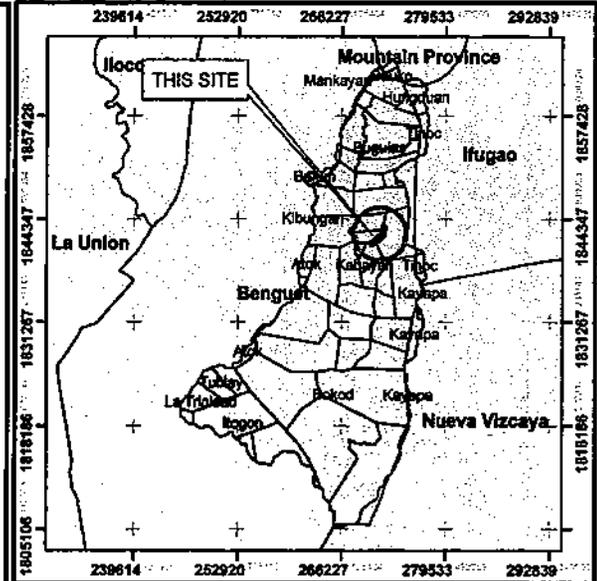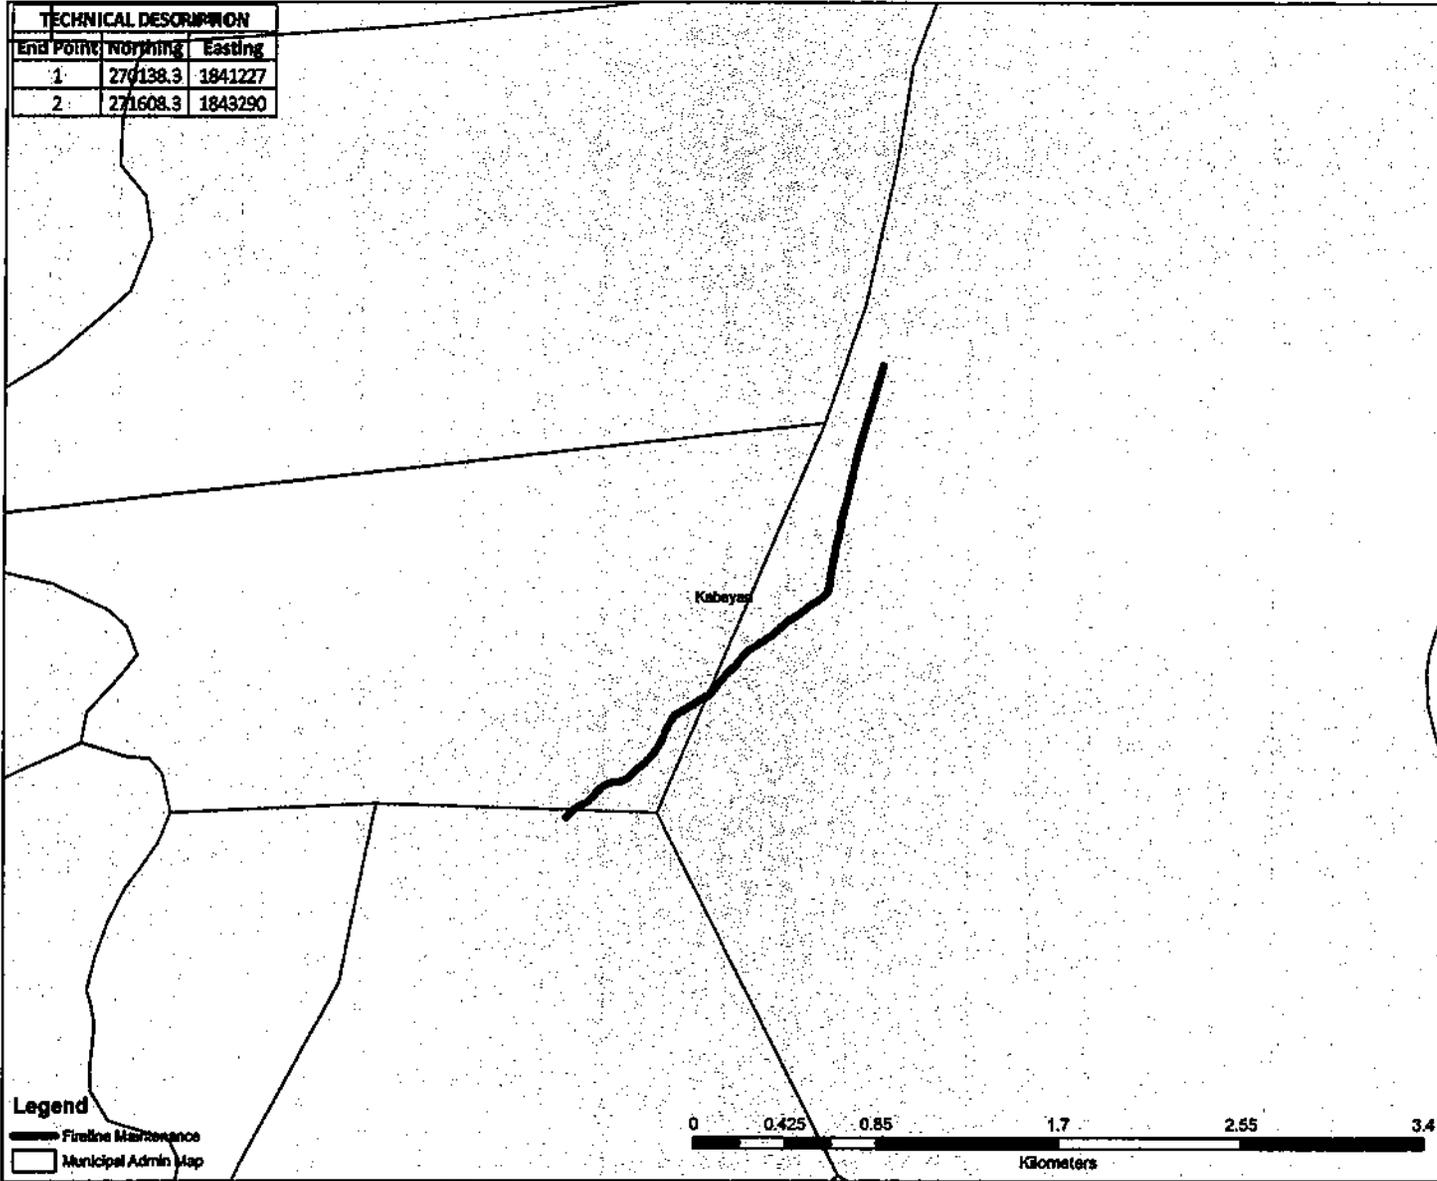

LOCATION MAP



Scale: 1:24,000

Map Projection:  
Universal Traverse Mercator (UTM) Zone 51N  
World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
Upper Agno River Watershed Area Team  
Watershed Management  
National Power Corporation

SITUATED IN THE:


BARANGAY OF: BANGAO TO GUSARAN  
MUN. / CITY OF: KABAYAN  
PROVINCE OF: BENGUET  
ISLAND OF: LUZON  
CONTAINING AN AREA OF: 5 LKM

**FINDINGS:**



1. VEGETATIVE COVER	<input type="checkbox"/> ADEQUATELY FORESTED	<input type="checkbox"/> INADEQUATELY STOCK
	<input type="checkbox"/> GRASSES/COGON	<input type="checkbox"/> BARED/DENUDED
2. TOPO SITUATION	<input type="checkbox"/> FLAT (0-18%)	<input type="checkbox"/> ROLLING (19-30%)
	<input type="checkbox"/> STEEP (>30%)	
3. OWNERSHIP	<input type="checkbox"/> CLAN/FAMILY	<input type="checkbox"/> ASSOCIATION
	<input type="checkbox"/> INDIVIDUAL	

4. REP/CONTROL POINTS	NO. _____
BUFFER MONUMENT	NO. _____
PUBLIC LAND	NO. _____
SUB-MONUMENT	NO. _____
CADASTRAL SURVEY	NO. _____
MONUMENT	
JUNCTION	
ROADS	
RIVERS	

**LAND-USE SURVEY MAPPING**

<p>PREPARED BY:</p> <p style="text-align: center;"> <b>MHERWIN B. CIPRIANO</b> Wat. Mgmt. Officer</p>	<p>NOTED BY:</p> <p style="text-align: center;"> <b>BENJAMIN T. KIMMAYONG</b> Section Chief-UARWAT</p>
--	---

TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	257914.07	1821552
2	254287.21	1811088.7

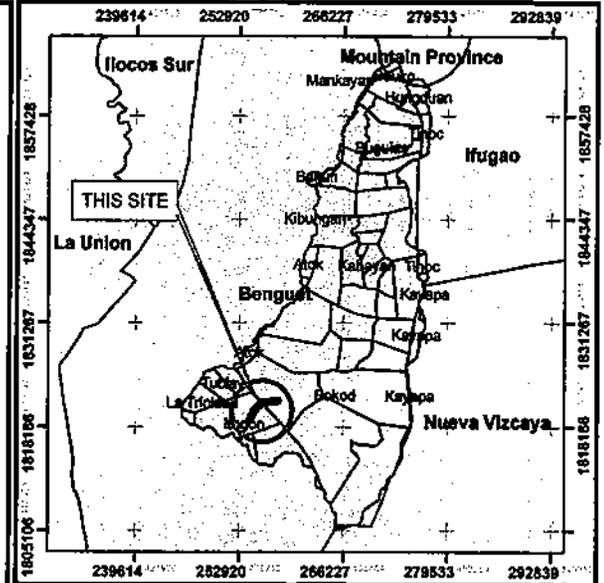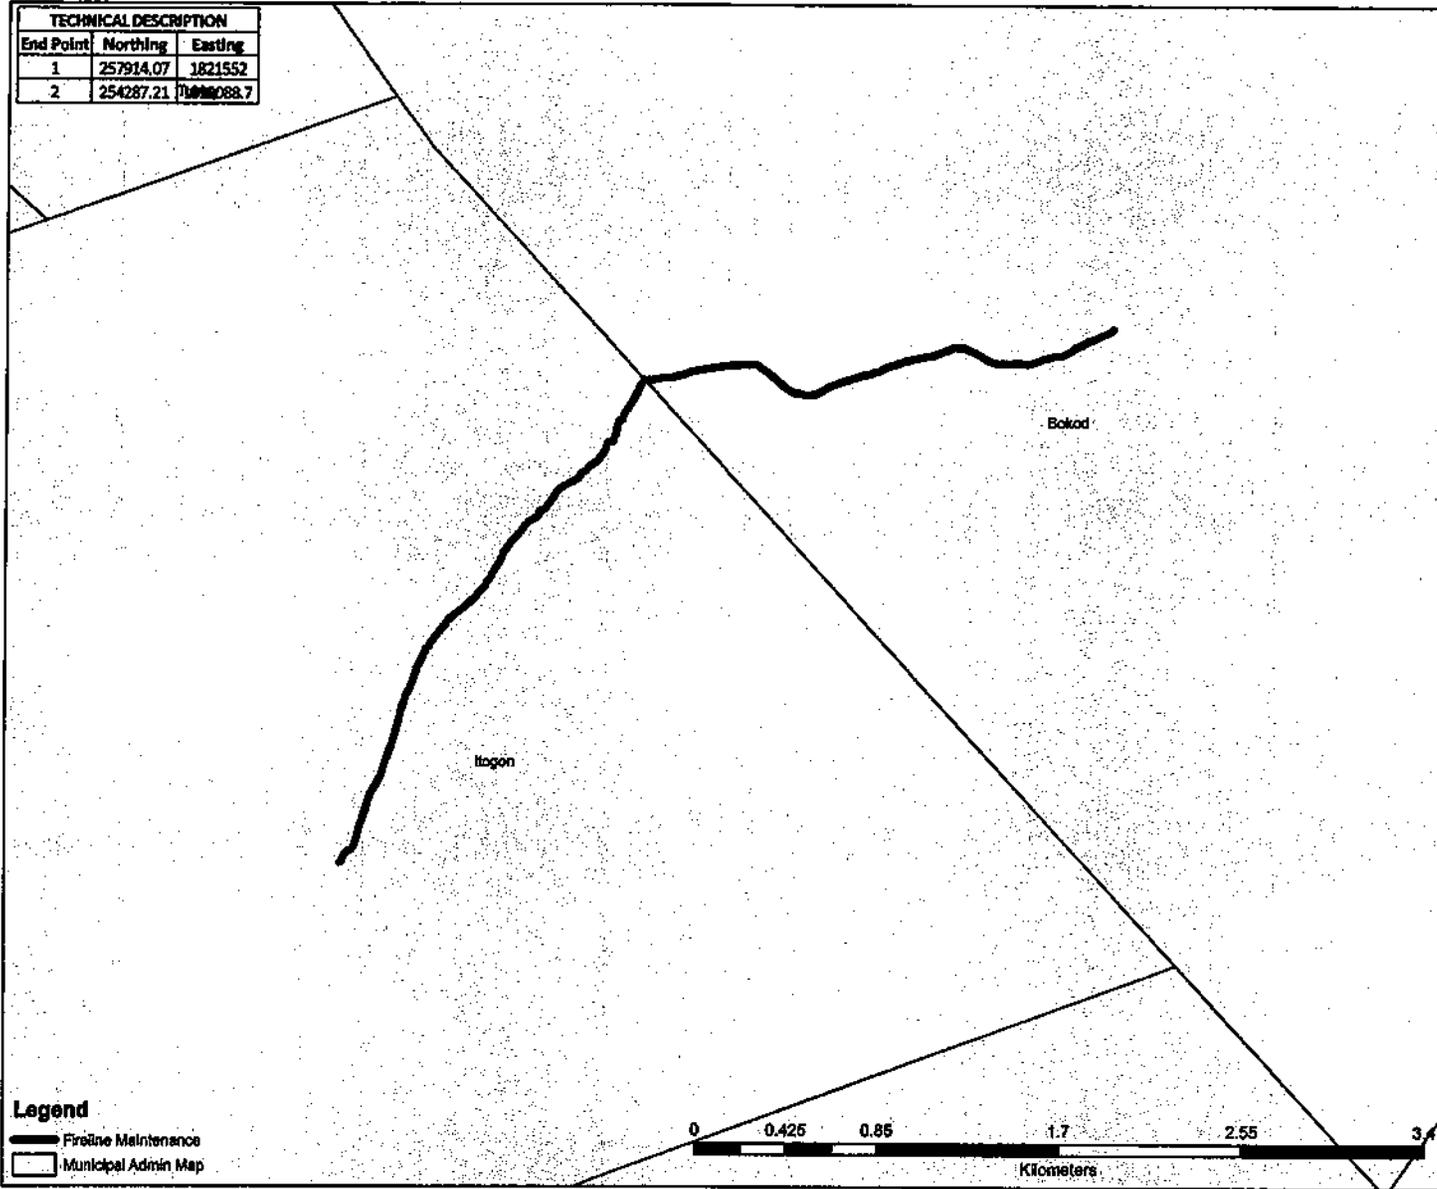

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
Upper Agno River Watershed Area Team  
Watershed Management  
National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: HILLTOP-MT. PATOKTOK-DUTAC  
MUN./CITY OF: BOKOD  
PROVINCE OF: BENGUET  
ISLAND OF: LUZON  
CONTAINING AN AREA OF: 5 LKM

**FINDINGS:**

**1. VEGETATIVE COVER**

- ADEQUATELY FORESTED
- INADEQUATELY STOCK
- GRASSES/COGON
- BARED/DENUDED

**2. TOPO SITUATION**

- FLAT (0-18%)
- ROLLING (19-30%)
- STEEP (>30%)

**3. OWNERSHIP**

- CLAN/FAMILY
- ASSOCIATION
- INDIVIDUAL

**4. REP/CONTROL POINTS**

- BUFFER MONUMENT NO. \_\_\_\_\_
- PUBLIC LAND SUB-MONUMENT NO. \_\_\_\_\_
- CADASTRAL SURVEY MONUMENT NO. \_\_\_\_\_
- JUNCTION \_\_\_\_\_
- ROADS \_\_\_\_\_
- RIVERS \_\_\_\_\_

**LAND-USE SURVEY MAPPING**


PREPARED BY:

*Mherwin C. Priano*  
MHERWIN C. PRIANO  
Wat. Mgmt. Officer


NOTED BY:

*Benjamin T. Kimmayong*  
BENJAMIN T. KIMMAYONG  
Section Chief-UARWAT


TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	264048.47	1826698.54
2	268516.04	1825237.34

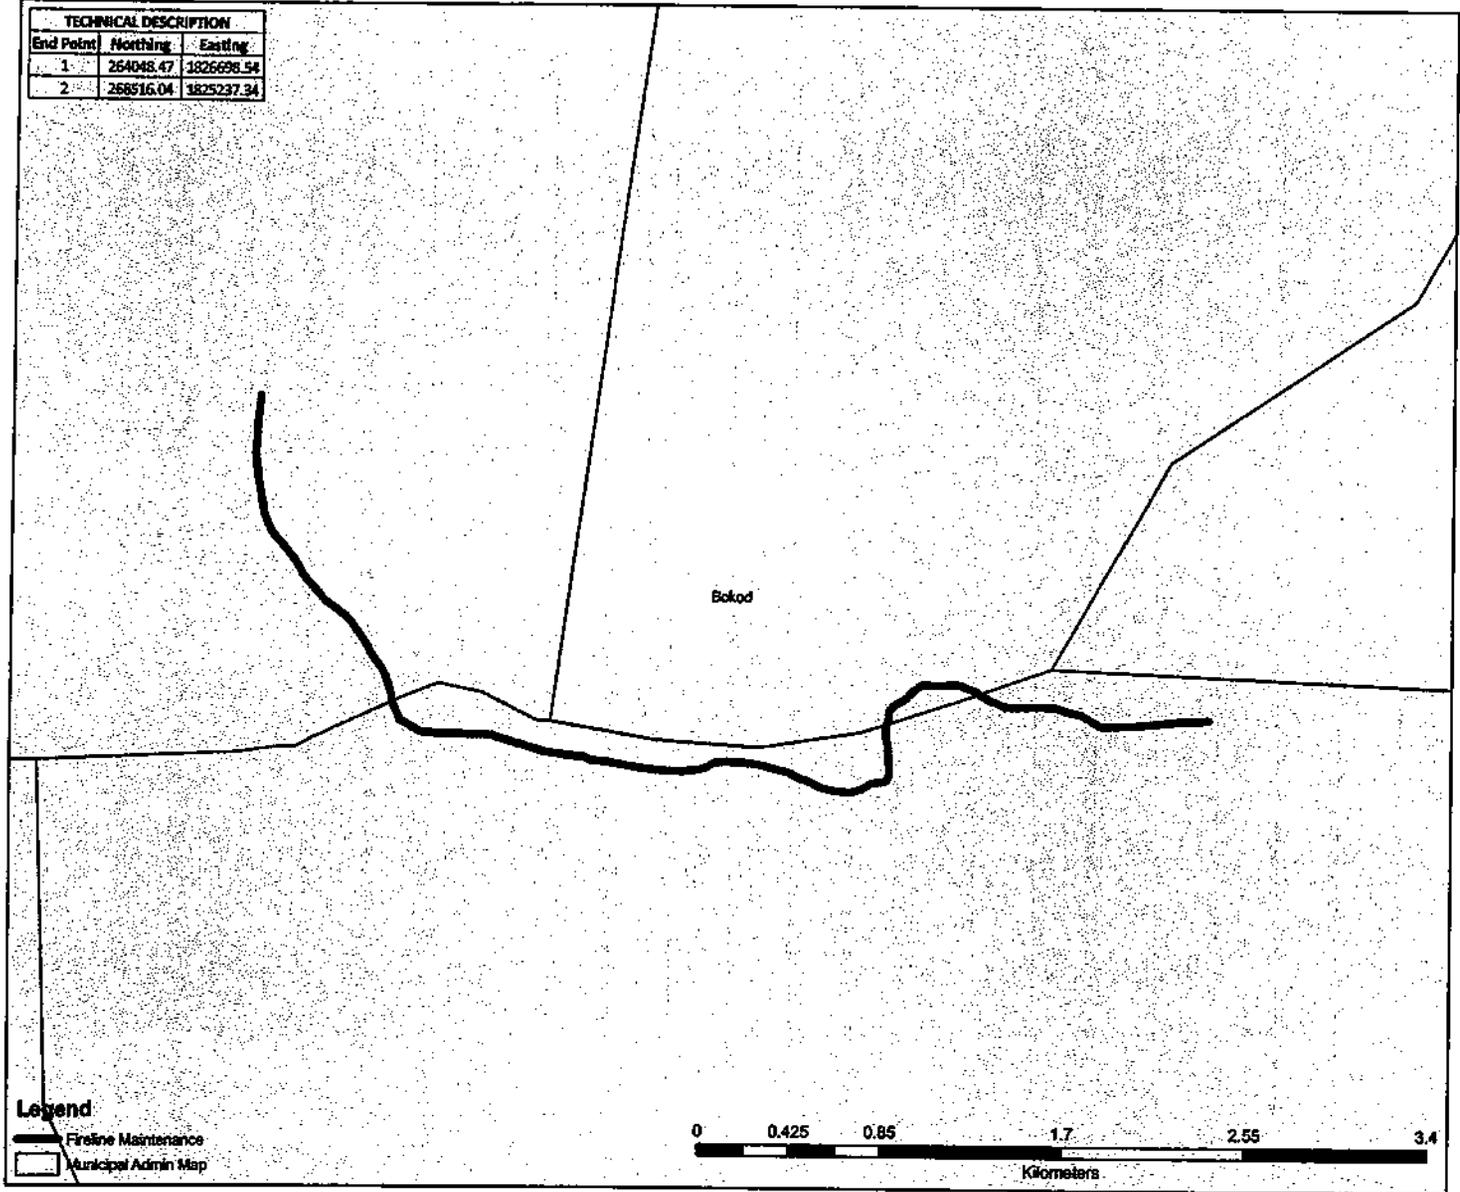

**Legend**  
 Fireline Maintenance  
 Municipal Admin Map

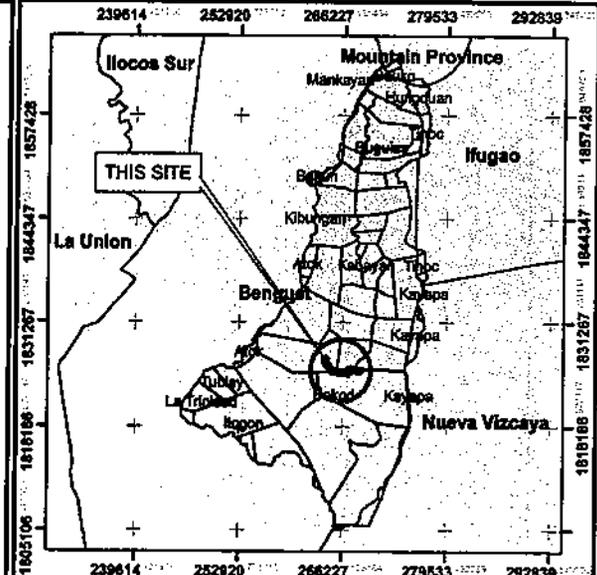

**LOCATION MAP**



Scale: 1:24,000  
 Map Projection:  
 Universal Traverse Mercator (UTM) Zone 51N  
 World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
 Upper Agno River Watershed Area Team  
 Watershed Management  
 National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: POBLACION TO BAGDAN  
 MUN. / CITY OF: BOKOD  
 PROVINCE OF: BENGUET  
 ISLAND OF: LUZON  
 CONTAINING AN AREA OF: 3 LKM


**FINDINGS:**

1. VEGETATIVE COVER	<input type="checkbox"/> ADEQUATELY FORESTED	<input type="checkbox"/> INADEQUATELY STOCK
	<input type="checkbox"/> GRASSES/COGON	<input type="checkbox"/> BARED/DENUDED
2. TOPO SITUATION	<input type="checkbox"/> FLAT (0-18%)	<input type="checkbox"/> ROLLING (19-30%)
	<input type="checkbox"/> STEEP (>30%)	
3. OWNERSHIP	<input type="checkbox"/> CLAN/FAMILY	<input type="checkbox"/> ASSOCIATION
	<input type="checkbox"/> INDIVIDUAL	


4. REP/CONTROL POINTS	NO. _____
BUFFER MONUMENT	NO. _____
PUBLIC LAND	NO. _____
SUB-MONUMENT	NO. _____
CADASTRAL SURVEY	NO. _____
MONUMENT	NO. _____
JUNCTION	NO. _____
ROADS	NO. _____
RIVERS	NO. _____

LAND-USE SURVEY MAPPING	
<b>PREPARED BY:</b>  MHERWIN B. CIPRIANO Wat. Mgmt. Officer	<b>NOTED BY:</b>  BENJAMIN T. KIMMAYONG Section Chief-UARWAT


TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	267707.86	1819657.55
2	264895.78	1822731.22

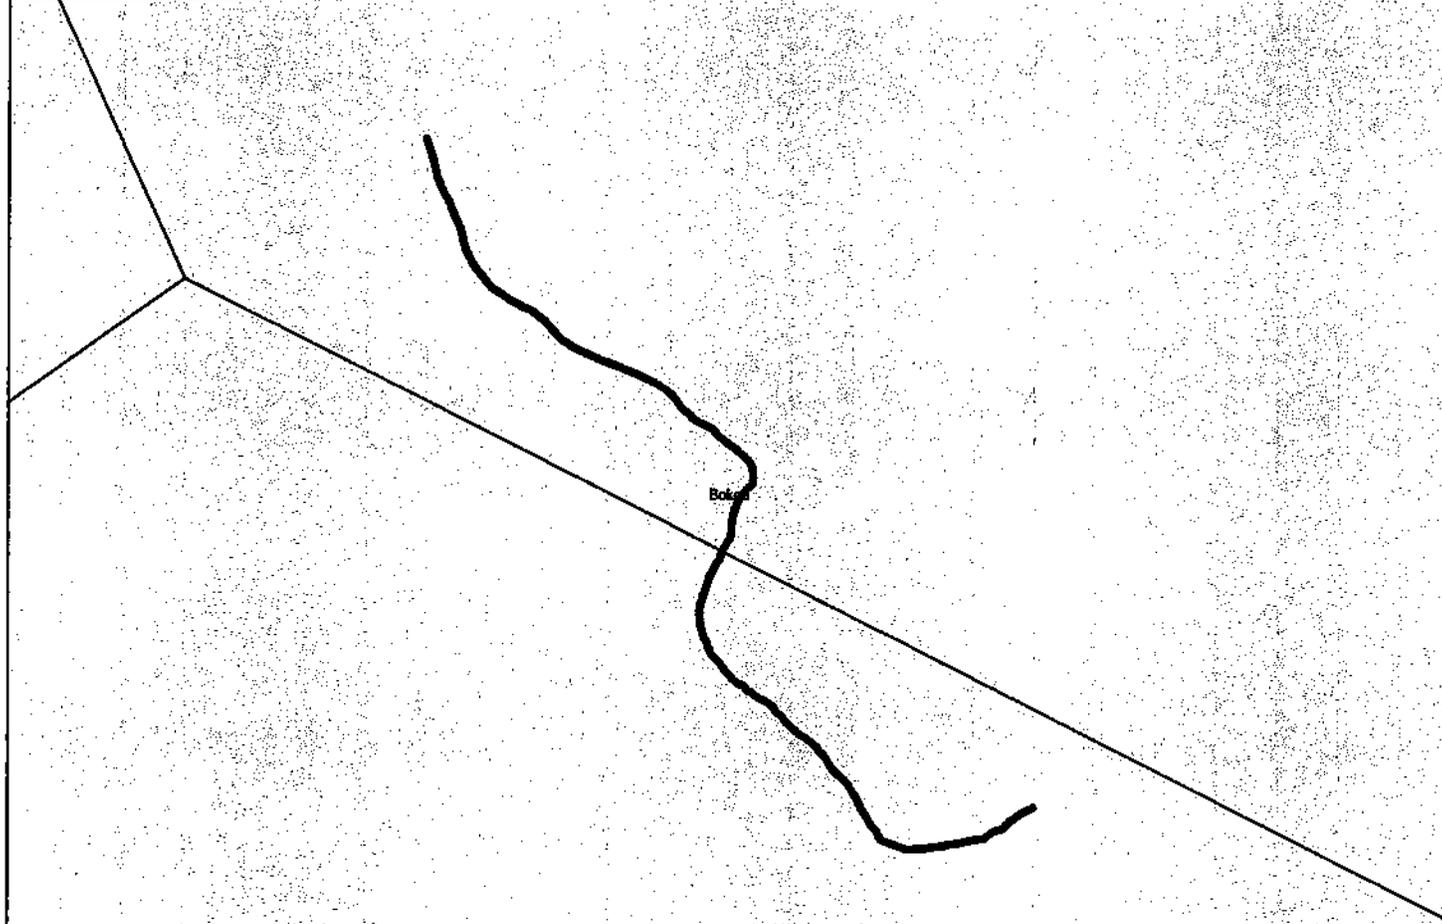

**Legend**  
 Fireline Maintenance  
 Municipal Admin Map

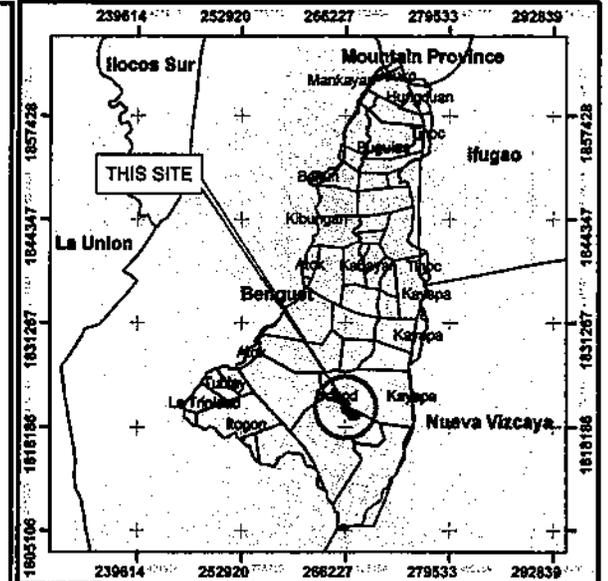

**LOCATION MAP**



Scale: 1:24,000

Map Projection:  
 Universal Transverse Mercator (UTM) Zone 51N  
 World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
 Upper Agno River Watershed Area Team  
 Watershed Management  
 National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: **BANGAO TO KAWAL**  
 MUN. / CITY OF: **BOKOD**  
 PROVINCE OF: **BENGUET**  
 ISLAND OF: **LUZON**  
 CONTAINING AN AREA OF: **4 LKM**

**FINDINGS:**

- |                     |  |   |
|---------------------|--|---|
| 1. VEGETATIVE COVER | <input type="checkbox"/> ADEQUATELY FORESTED | <input type="checkbox"/> INADEQUATELY STOCK |
|                     | <input type="checkbox"/> GRASSES/COGON       | <input type="checkbox"/> BARED/DENUDED      |
| 2. TOPO SITUATION   | <input type="checkbox"/> FLAT (0-18%)        | <input type="checkbox"/> ROLLING (19-30%)   |
|                     | <input type="checkbox"/> STEEP (>30%)        |   |
| 3. OWNERSHIP        | <input type="checkbox"/> CLAN/FAMILY         | <input type="checkbox"/> ASSOCIATION        |
|                     | <input type="checkbox"/> INDIVIDUAL          |   |

- |                       |           |
|-----------------------|-----------|
| 4. REP/CONTROL POINTS | NO. _____ |
| BUFFER MONUMENT       | NO. _____ |
| PUBLIC LAND           | NO. _____ |
| SUB-MONUMENT          | NO. _____ |
| CADASTRAL SURVEY      | NO. _____ |
| MONUMENT              |           |
| JUNCTION              |           |
| _____ ROADS           |           |
| _____ RIVERS          |           |

**LAND-USE SURVEY MAPPING**


PREPARED BY:

**MHERWIN S. CIPRIANO**  
 Wat. Mgmt. Officer



NOTED BY:

**BENJAMIN T. KIMMAYONG**  
 Section Chief-UARWAT

TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	261198.9	1822691.32
2	260450.5	1819257.52

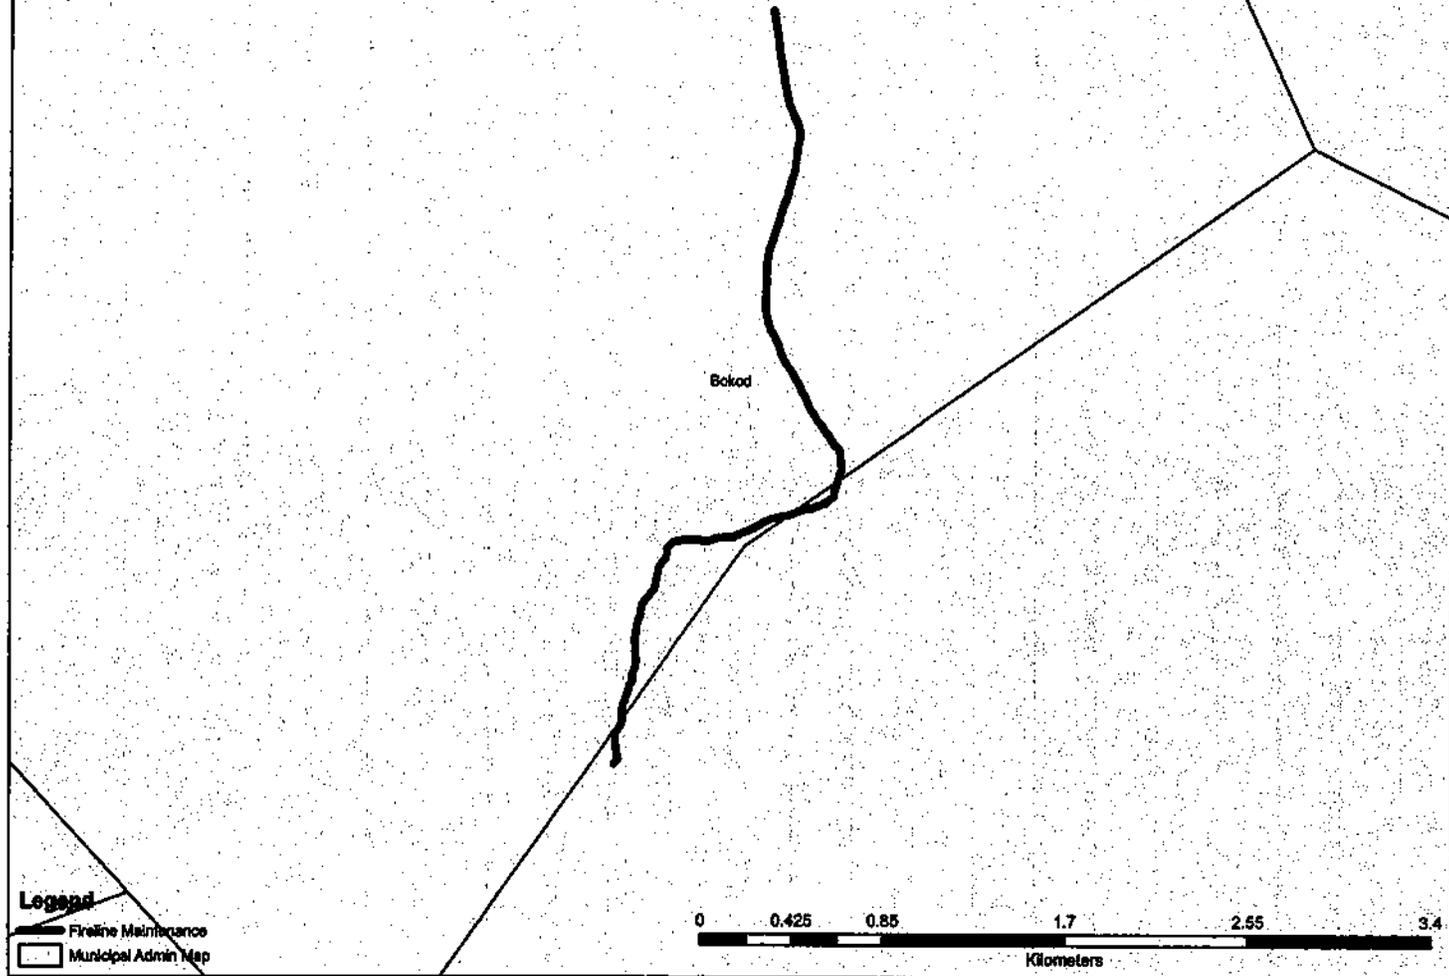

**Legend**  
 Fireline Maintenance  
 Municipal Admin Map

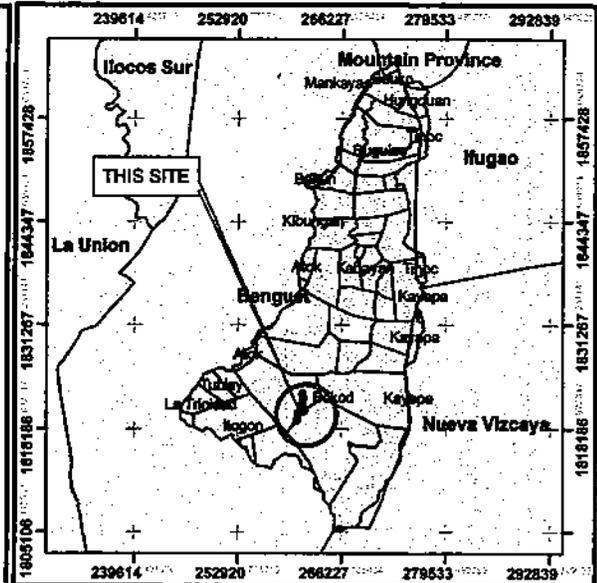

**LOCATION MAP**



Scale: 1:24,000  
 Map Projection:  
 Universal Transverse Mercator (UTM) Zone 51N  
 World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
 Upper Agno River Watershed Area Team  
 Watershed Management  
 National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: INDIAN TO DAMSHACK  
 MUN. / CITY OF: BOKOD  
 PROVINCE OF: BENGUET  
 ISLAND OF: LUZON  
 CONTAINING AN AREA OF: 4 LKM

**FINDINGS:**



1. VEGETATIVE COVER	<input type="checkbox"/> ADEQUATELY FORESTED	<input type="checkbox"/> INADEQUATELY STOCK
	<input type="checkbox"/> GRASSES/COGON	<input type="checkbox"/> BARED/DENUDED
2. TOPO SITUATION	<input type="checkbox"/> FLAT (0-18%)	<input type="checkbox"/> ROLLING (19-30%)
	<input type="checkbox"/> STEEP (>30%)	
3. OWNERSHIP	<input type="checkbox"/> CLAN/FAMILY	<input type="checkbox"/> ASSOCIATION
	<input type="checkbox"/> INDIVIDUAL	

4. REP/CONTROL POINTS	NO. _____
BUFFER MONUMENT	NO. _____
PUBLIC LAND	NO. _____
SUB-MONUMENT	NO. _____
CADASTRAL SURVEY	NO. _____
MONUMENT	
JUNCTION	
ROADS	
RIVERS	

**LAND-USE SURVEY MAPPING**

<p><b>PREPARED BY:</b></p> <p style="text-align: center;">  <b>MHERWIN L. CIPRIANO</b>          Wat. Mgmt. Officer</p>	<p><b>NOTED BY:</b></p> <p style="text-align: center;">  <b>BENJAMIN T. KIMMAYONG</b>          Section Chief-UARWAT</p>
--	---

TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	254842.8	1822491
2	255262.8	1818054

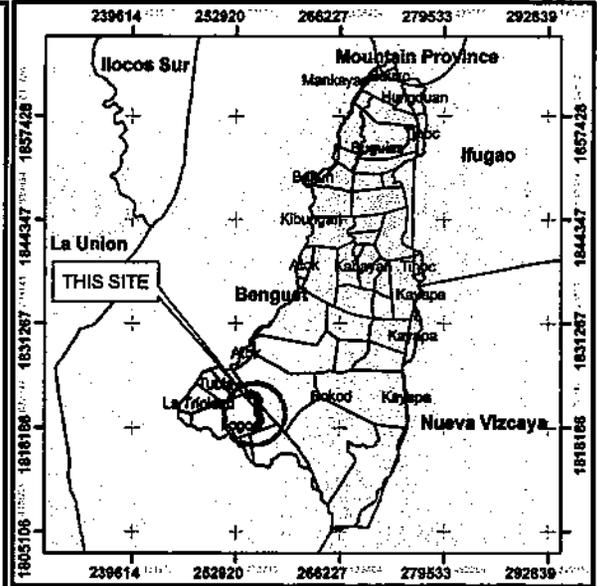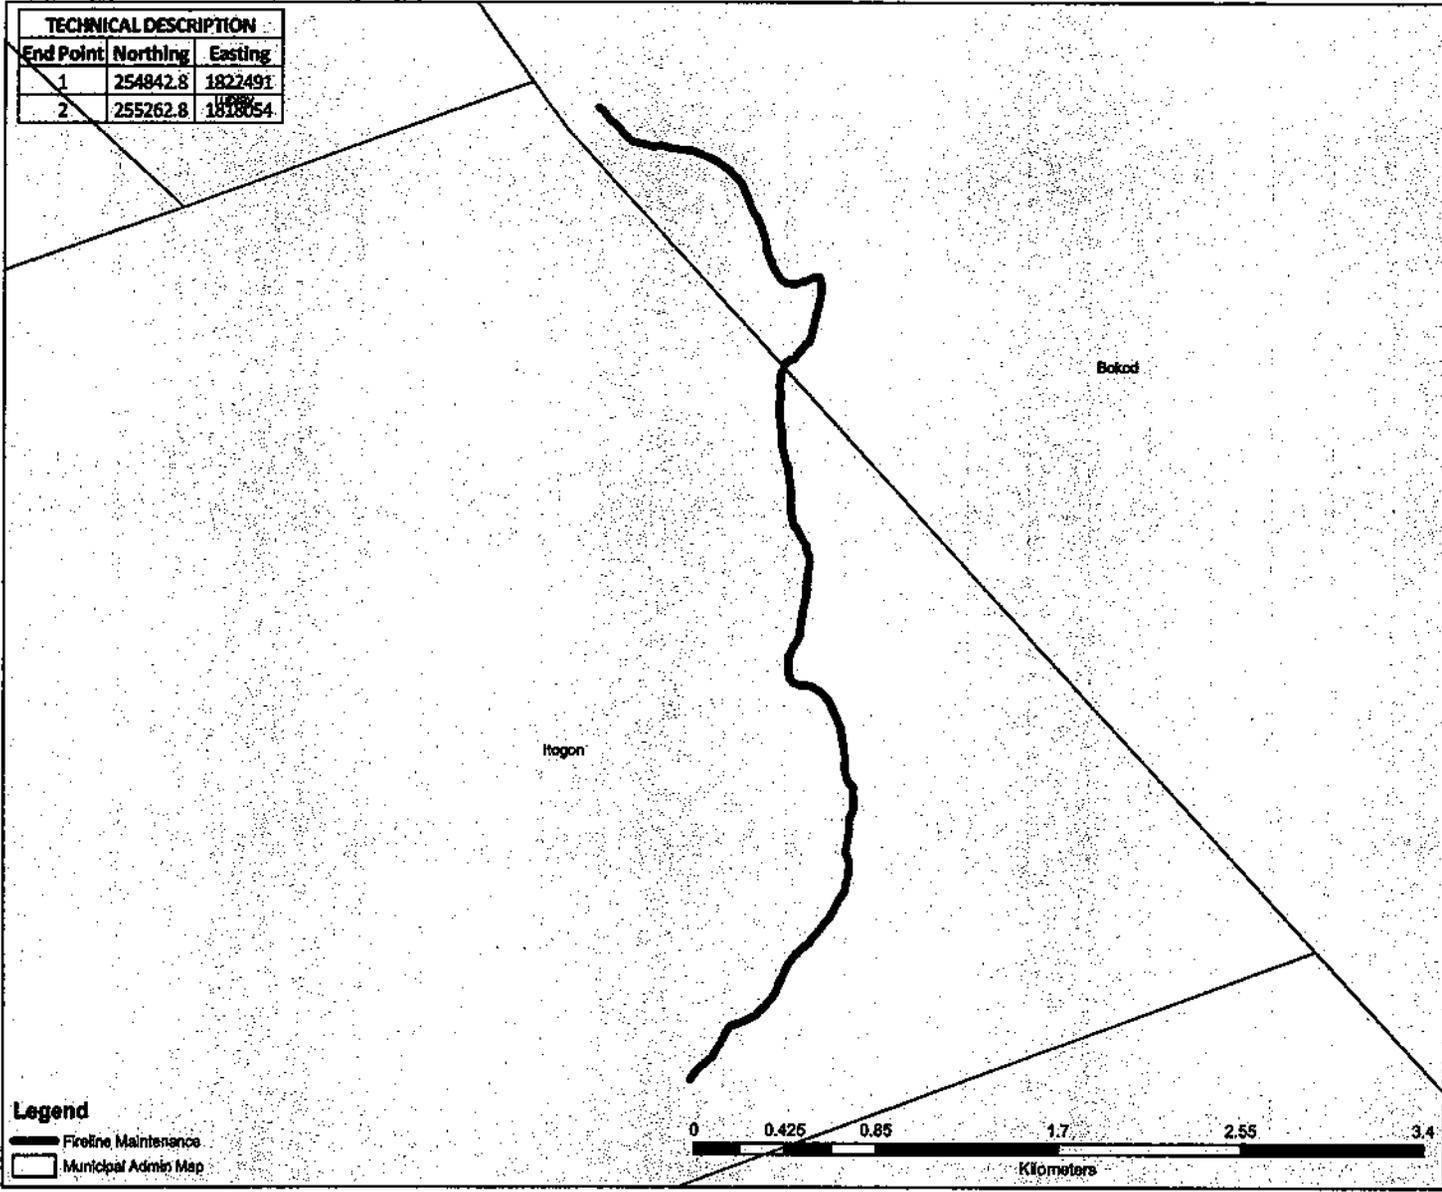

**LOCATION MAP**

N  
W — E  
S

Scale: 1:24,000  
Map Projection:  
Universal Transverse Mercator (UTM) Zone 51N  
World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**  
AS PREPARED FOR  
Upper Agno River Watershed Area Team  
Watershed Management  
National Power Corporation

**SITUATED IN THE:**  
BARANGAY OF: GEWENG TO ADONOT  
MUN. / CITY OF: BOKOD  
PROVINCE OF: BENGUET  
ISLAND OF: LUZON  
CONTAINING AN AREA OF: 4 LKM

**FINDINGS:**

1. VEGETATIVE COVER  
 ADEQUATELY FORESTED     INADEQUATELY STOCK  
 GRASSES/COGON             BAREO/DENUDED

2. TOPO SITUATION  
 FLAT (0-18%)     ROLLING (19-30%)     STEEP (>30%)

3. OWNERSHIP  
 CLAN/FAMILY     ASSOCIATION     INDIVIDUAL



4. REP/CONTROL POINTS  
 BUFFER MONUMENT    NO. \_\_\_\_\_  
 PUBLIC LAND  
 SUB-MONUMENT        NO. \_\_\_\_\_  
 CADASTRAL SURVEY  
 MONUMENT            NO. \_\_\_\_\_  
 JUNCTION  
 \_\_\_\_\_ ROADS  
 \_\_\_\_\_ RIVERS

**LAND-USE SURVEY MAPPING**

**PREPARED BY:**  
  
**MHERWIN E. CIPRIANO**  
 Wat. Mgmt. Officer

**NOTED BY:**  
  
**BENJAMIN T. KIMMAYONG**  
 Section Chief-UARWAT

TECHNICAL DESCRIPTION		
End Point	Northings	Eastings
1	254465.31	1826192.56
2	258763.63	1825392.14

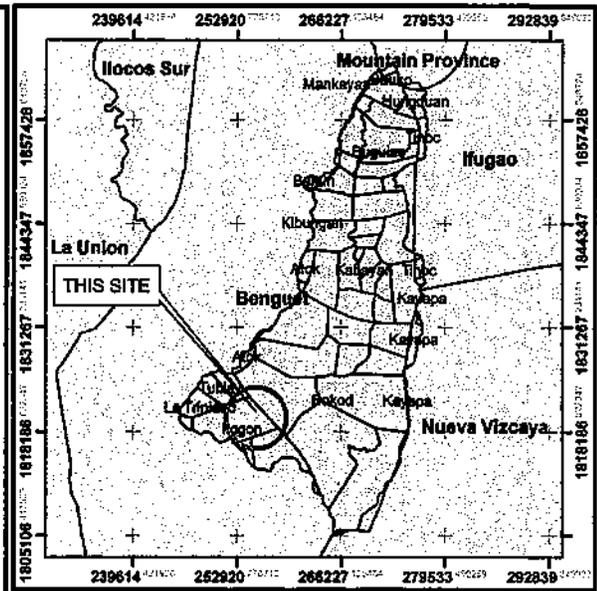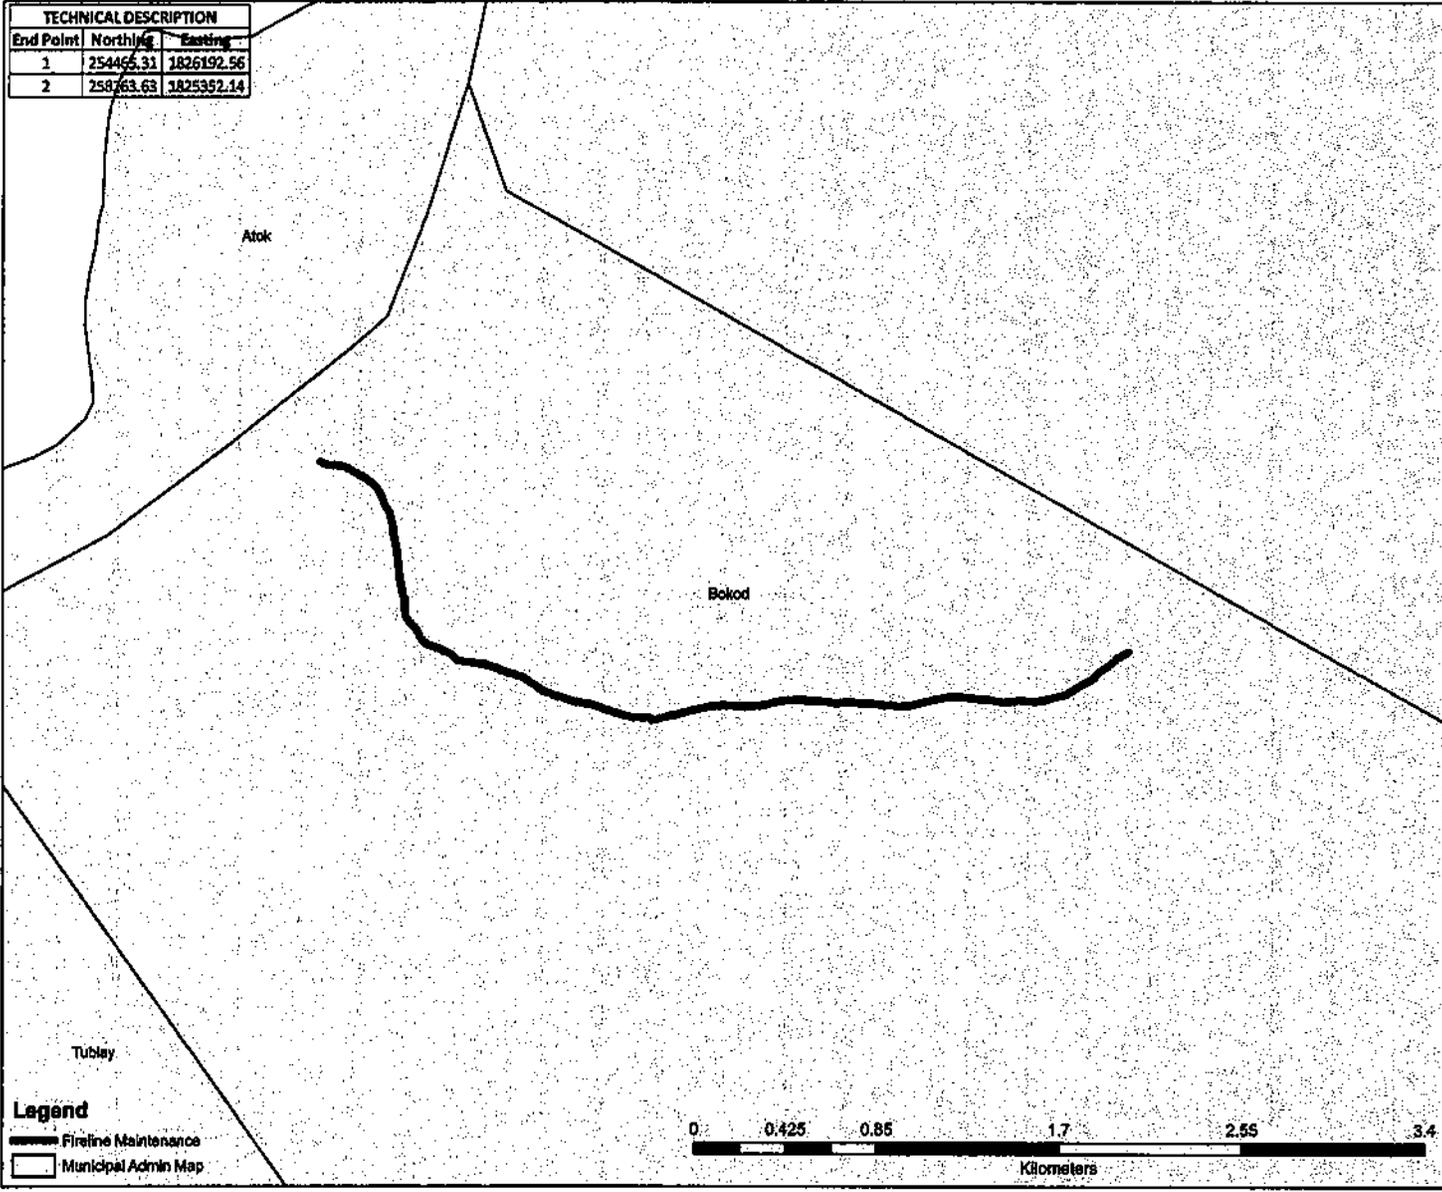

**LOCATION MAP**

N  
W — E  
S

Scale: 1:24,000  
Map Projection:  
Universal Traverse Mercator (UTM) Zone 51N  
World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**  
AS PREPARED FOR  
Upper Agno River Watershed Area Team  
Watershed Management  
National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: ALAM-AM TO SUGEL  
MUN./CITY OF: BOKOD  
PROVINCE OF: BENGUET  
ISLAND OF: LUZON  
CONTAINING AN AREA OF: 4 LKM



- FINDINGS:**
- |                     |  |   |
|---------------------|--|---|
| 1. VEGETATIVE COVER | <input type="checkbox"/> ADEQUATELY FORESTED | <input type="checkbox"/> INADEQUATELY STOCK |
|                     | <input type="checkbox"/> GRASSES/COGON       | <input type="checkbox"/> BARED/DENUDED      |
| 2. TOPO SITUATION   | <input type="checkbox"/> FLAT (0-18%)        | <input type="checkbox"/> ROLLING (19-30%)   |
|                     | <input type="checkbox"/> STEEP (>30%)        |   |
| 3. OWNERSHIP        | <input type="checkbox"/> CLAN/FAMILY         | <input type="checkbox"/> ASSOCIATION        |
|                     | <input type="checkbox"/> INDIVIDUAL          |   |

- |                       |           |
|-----------------------|-----------|
| 4. REP/CONTROL POINTS | NO. _____ |
| BUFFER MONUMENT       | NO. _____ |
| PUBLIC LAND           | NO. _____ |
| SUB-MONUMENT          | NO. _____ |
| CADASTRAL SURVEY      | NO. _____ |
| MONUMENT              |           |
| JUNCTION              |           |
| _____ ROADS           |           |
| _____ RIVERS          |           |

**LAND-USE SURVEY MAPPING**

<p><b>PREPARED BY:</b></p> <p style="text-align: center;"><i>[Signature]</i> <b>MHERWIN B. CIPRIANO</b> Wat. Mgmt. Officer</p>	<p><b>NOTED BY:</b></p> <p style="text-align: center;"><i>[Signature]</i> <b>BENJAMIN T. KIMMAYONG</b> Section Chief-UARWAT</p>
--	---

TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	260143.6	1819386
2	258765.9	1814517

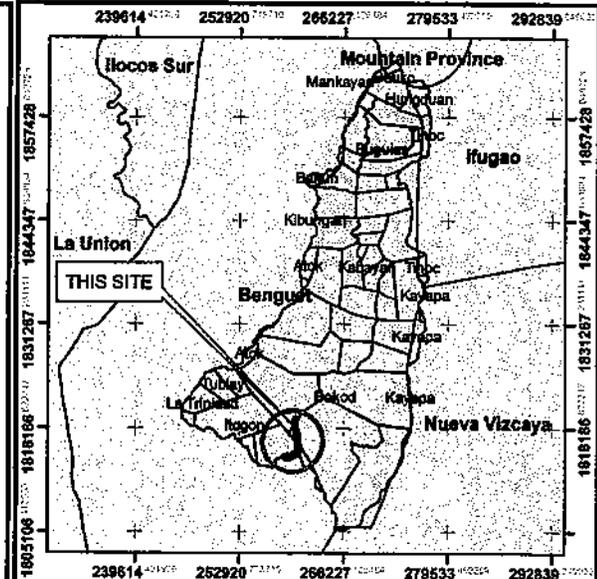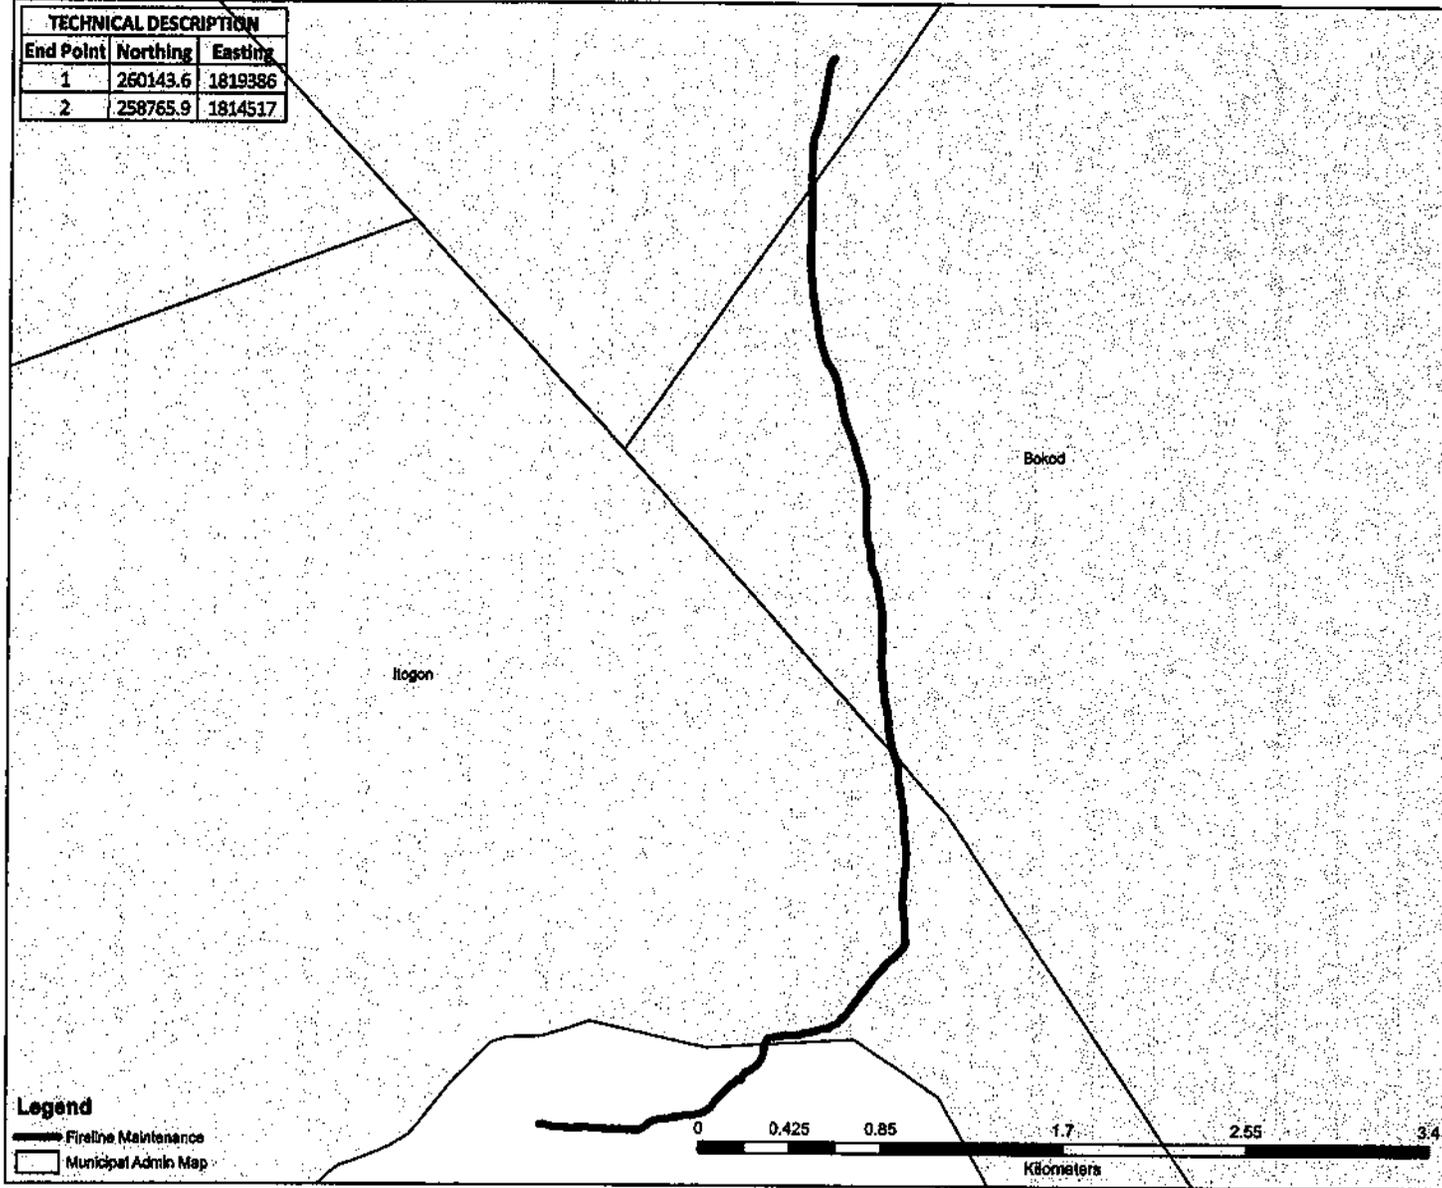

**LOCATION MAP**



Scale: 1:24,000

Map Projection:  
Universal Transverse Mercator (UTM) Zone 51N  
World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
Upper Agno River Watershed Area Team  
Watershed Management  
National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: **COMODIAN TO PALEW**  
MUN. / CITY OF: **ITOGON**  
PROVINCE OF: **BENGUET**  
ISLAND OF: **LUZON**  
CONTAINING AN AREA OF: **4 LKM**

**FINDINGS:**

- |                     |  |   |
|---------------------|--|---|
| 1. VEGETATIVE COVER | <input type="checkbox"/> ADEQUATELY FORESTED | <input type="checkbox"/> INADEQUATELY STOCK |
|                     | <input type="checkbox"/> GRASSES/COGON       | <input type="checkbox"/> BARED/DENUDED      |
| 2. TOPO SITUATION   | <input type="checkbox"/> FLAT (0-18%)        | <input type="checkbox"/> ROLLING (19-30%)   |
|                     | <input type="checkbox"/> STEEP (>30%)        |   |
| 3. OWNERSHIP        | <input type="checkbox"/> CLAN/FAMILY         | <input type="checkbox"/> ASSOCIATION        |
|                     | <input type="checkbox"/> INDIVIDUAL          |   |

- |                       |           |
|-----------------------|-----------|
| 4. REP/CONTROL POINTS | NO. _____ |
| BUFFER MONUMENT       |           |
| PUBLIC LAND           |           |
| SUB-MONUMENT          | NO. _____ |
| CADASTRAL SURVEY      |           |
| MONUMENT              | NO. _____ |
| JUNCTION              |           |
| ROADS                 |           |
| RIVERS                |           |

**LAND-USE SURVEY MAPPING**


PREPARED BY:

MHERWIN S. CIPRIANO  
Wat. Mgrt. Officer

NOTED BY:


BENJAMIN T. KIMMAYONG  
Section Chief-UARWAT

TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	255732.83	1812149.88
2	253919.88	1815615.56

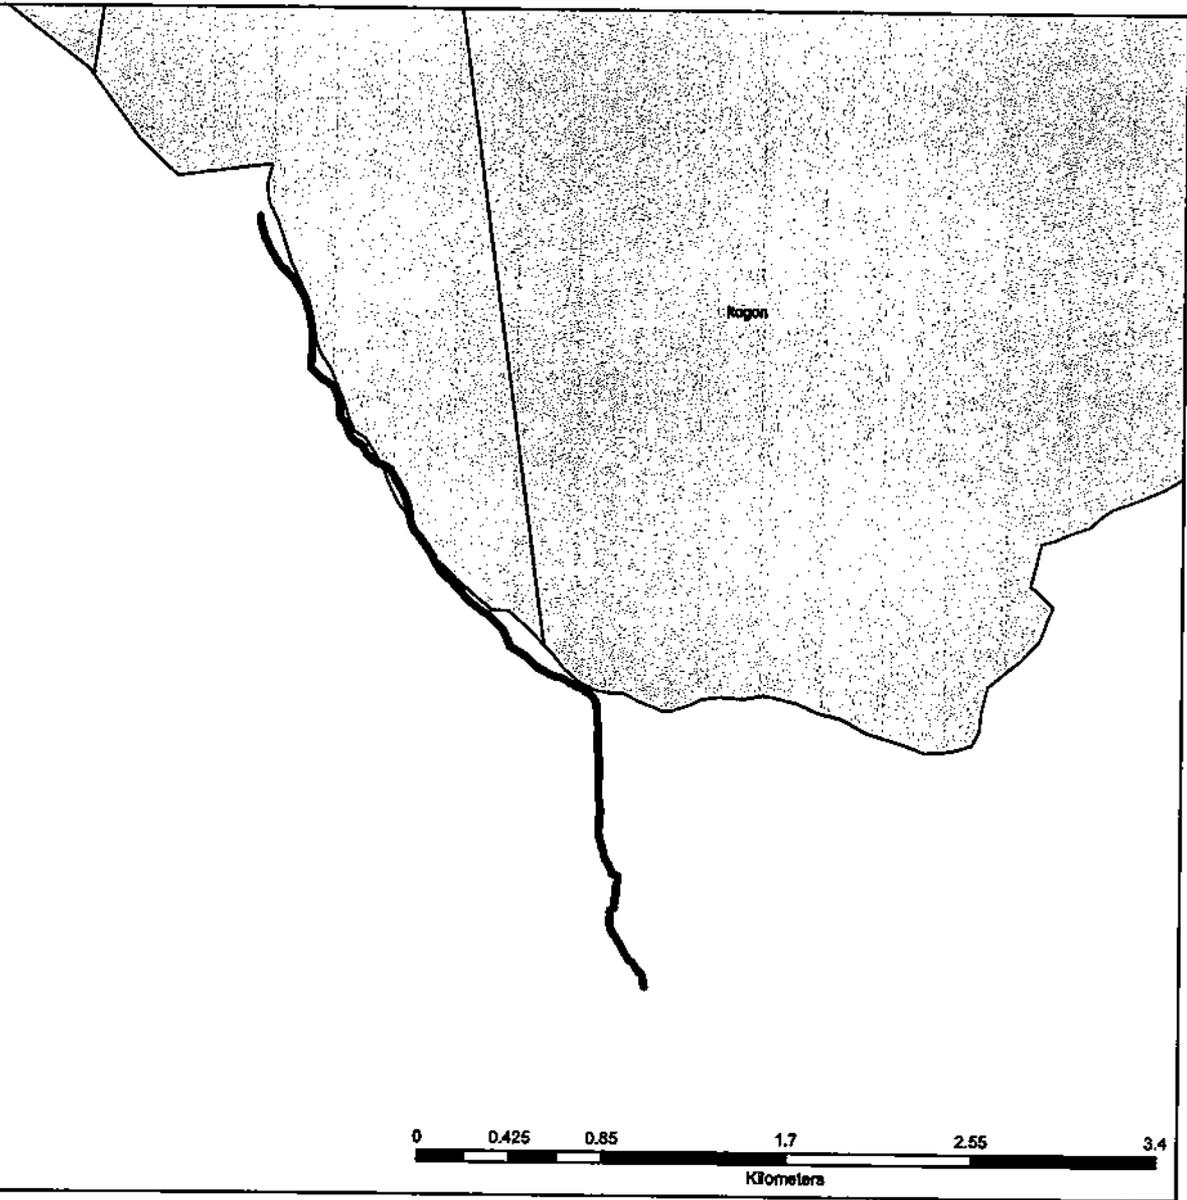


**Legend**

- Fireline Maintenance
- Municipal Admin Map

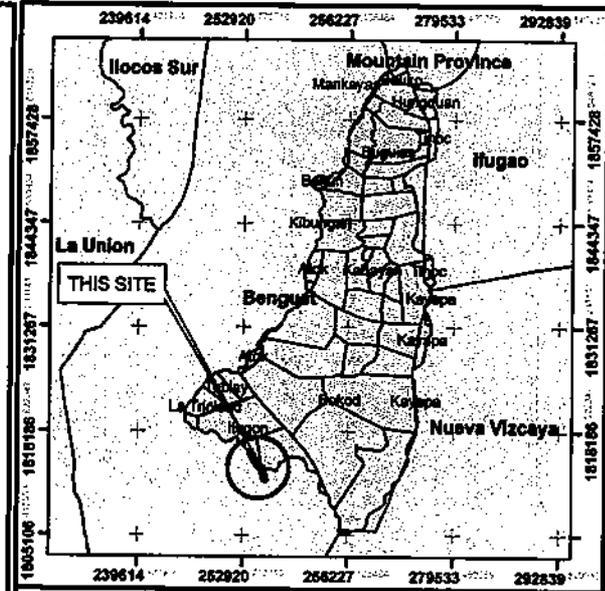

**LOCATION MAP**



Scale: 1:24,000  
 Map Projection:  
 Universal Traverse Mercator (UTM) Zone 51N  
 World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
 Upper Agno River Watershed Area Team  
 Watershed Management  
 National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: BALOY TO CAMISONG  
 MUN. / CITY OF: ITOGON  
 PROVINCE OF: BENGUET  
 ISLAND OF: LUZON  
 CONTAINING AN AREA OF: 4 LKM

**FINDINGS:**

1. VEGETATIVE COVER	<input type="checkbox"/> ADEQUATELY FORESTED	<input type="checkbox"/> INADEQUATELY STOCK
	<input type="checkbox"/> GRASSES/COGON	<input type="checkbox"/> BARED/DENUDED
2. TOPO SITUATION	<input type="checkbox"/> FLAT (0-18%)	<input type="checkbox"/> ROLLING (19-30%)
	<input type="checkbox"/> STEEP (>30%)	
3. OWNERSHIP	<input type="checkbox"/> CLAN/FAMILY	<input type="checkbox"/> ASSOCIATION
	<input type="checkbox"/> INDIVIDUAL	

4. REP/CONTROL POINTS	NO. _____
BUFFER MONUMENT	NO. _____
PUBLIC LAND	NO. _____
SUB-MONUMENT	NO. _____
CADASTRAL SURVEY	NO. _____
MONUMENT	
JUNCTION	
ROADS	
RIVERS	

**LAND-USE SURVEY MAPPING**



**PREPARED BY:**

**MHERWIN A. CIPRIANO**  
 Wat. Mgmt. Officer

**NOTED BY:**

**BENJAMIN T. KIMMAYONG**  
 Section Chief-UARWAT

TYPICAL DESCRIPTION		
Spot Point	Northing	Easting
1	251205.73	1817065.52
2	254168.15	1819536.65

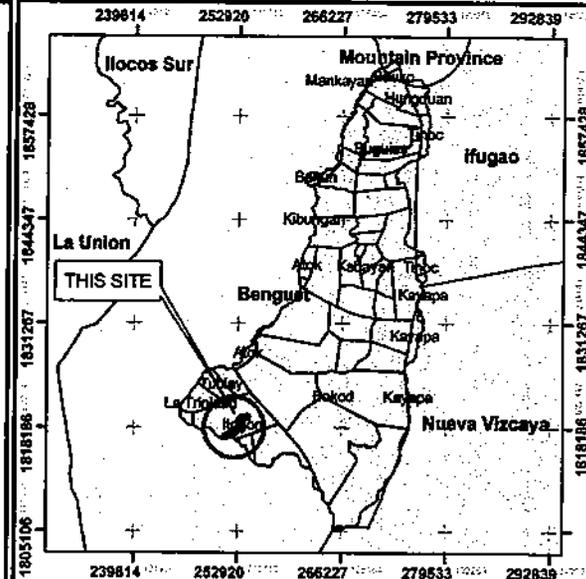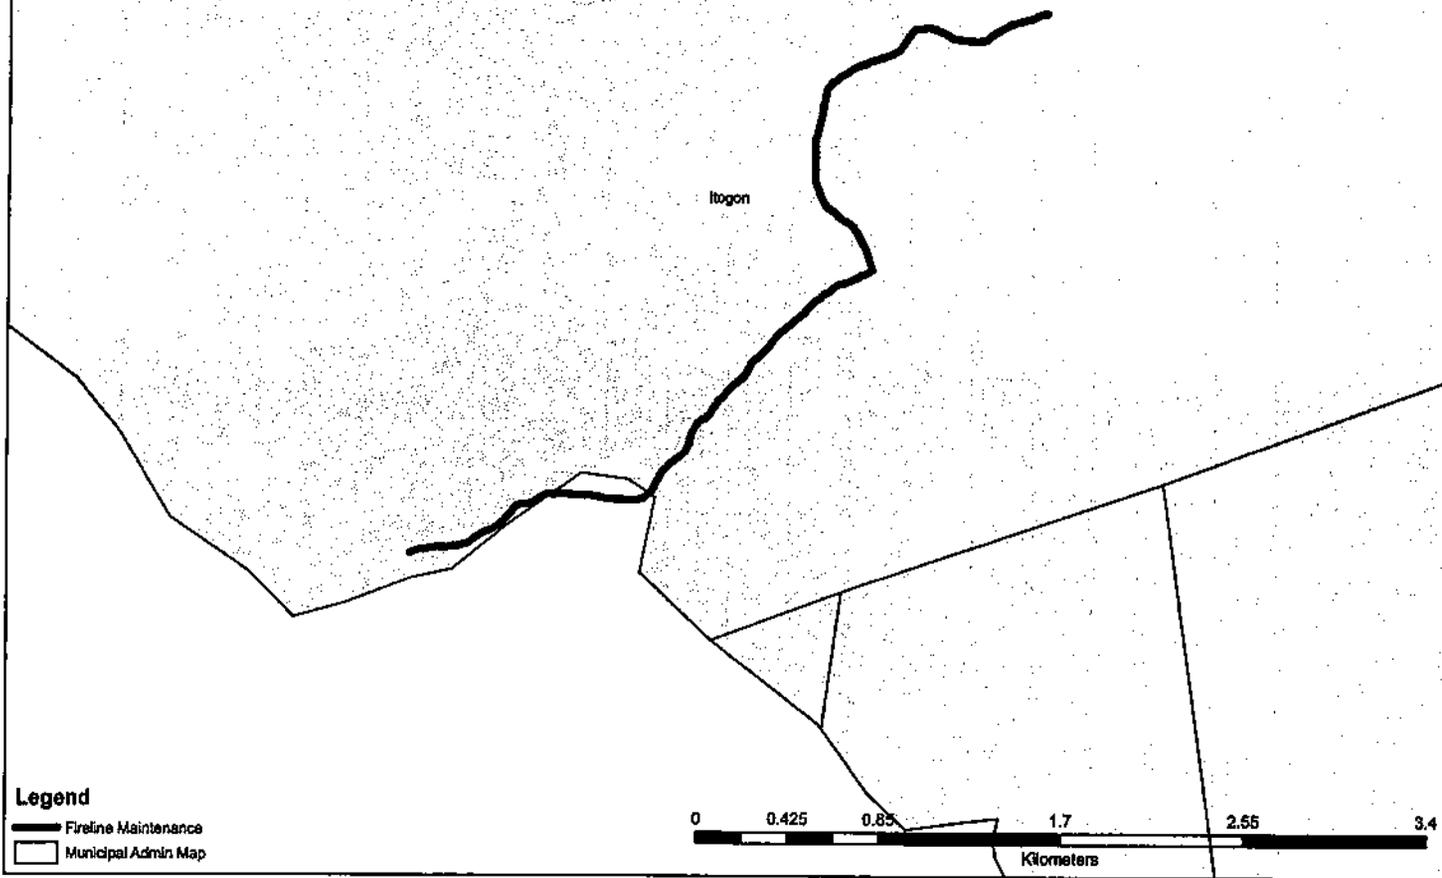

**LOCATION MAP**



Scale: 1:24,000

Map Projection:  
Universal Traverse Mercator (UTM) Zone 51N  
World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**

AS PREPARED FOR  
Upper Agno River Watershed Area Team  
Watershed Management  
National Power Corporation

**SITUATED IN THE:**

BARANGAY OF: MARO-OC TO SAITAN  
MUN./CITY OF: ITOGON  
PROVINCE OF: BENGUET  
ISLAND OF: LUZON  
CONTAINING AN AREA OF: 4 LKM

**FINDINGS:**

1. VEGETATIVE COVER	<input type="checkbox"/> ADEQUATELY FORESTED	<input type="checkbox"/> INADEQUATELY STOCK
	<input type="checkbox"/> GRASSES/COGON	<input type="checkbox"/> BARED/DENUDED
2. TOPO SITUATION	<input type="checkbox"/> FLAT (0-18%)	<input type="checkbox"/> ROLLING (19-30%)
	<input type="checkbox"/> STEEP (>30%)	
3. OWNERSHIP	<input type="checkbox"/> CLAN/FAMILY	<input type="checkbox"/> ASSOCIATION
	<input type="checkbox"/> INDIVIDUAL	



4. REP/CONTROL POINTS	NO. _____
BUFFER MONUMENT	NO. _____
PUBLIC LAND	NO. _____
SUB-MONUMENT	NO. _____
CADASTRAL SURVEY	NO. _____
MONUMENT	
JUNCTION	
_____ ROADS	
_____ RIVERS	

**LAND-USE SURVEY MAPPING**

**PREPARED BY:**  
  
MHERWIN B. CIPRIANO  
Wat. Mgmt. Officer

**NOTED BY:**  
  
BENJAMIN T. KIMMAYONG  
Section Chief-UARWAT

TECHNICAL DESCRIPTION		
End Point	Northing	Easting
1	267918.8	1823229.62
2	271549.5	1825578.85

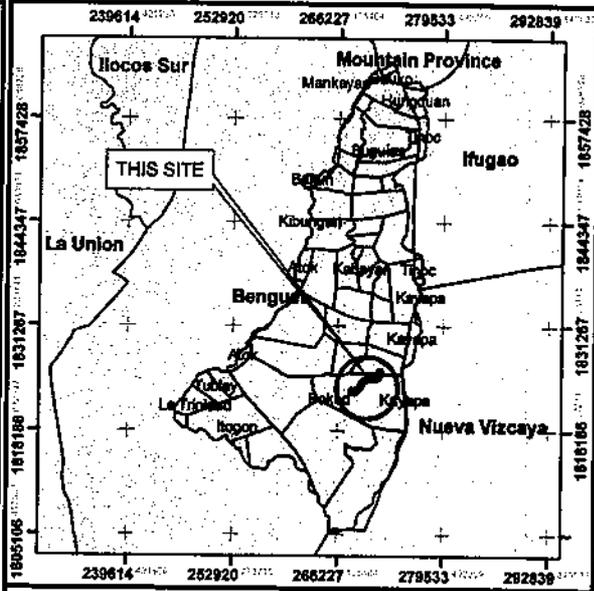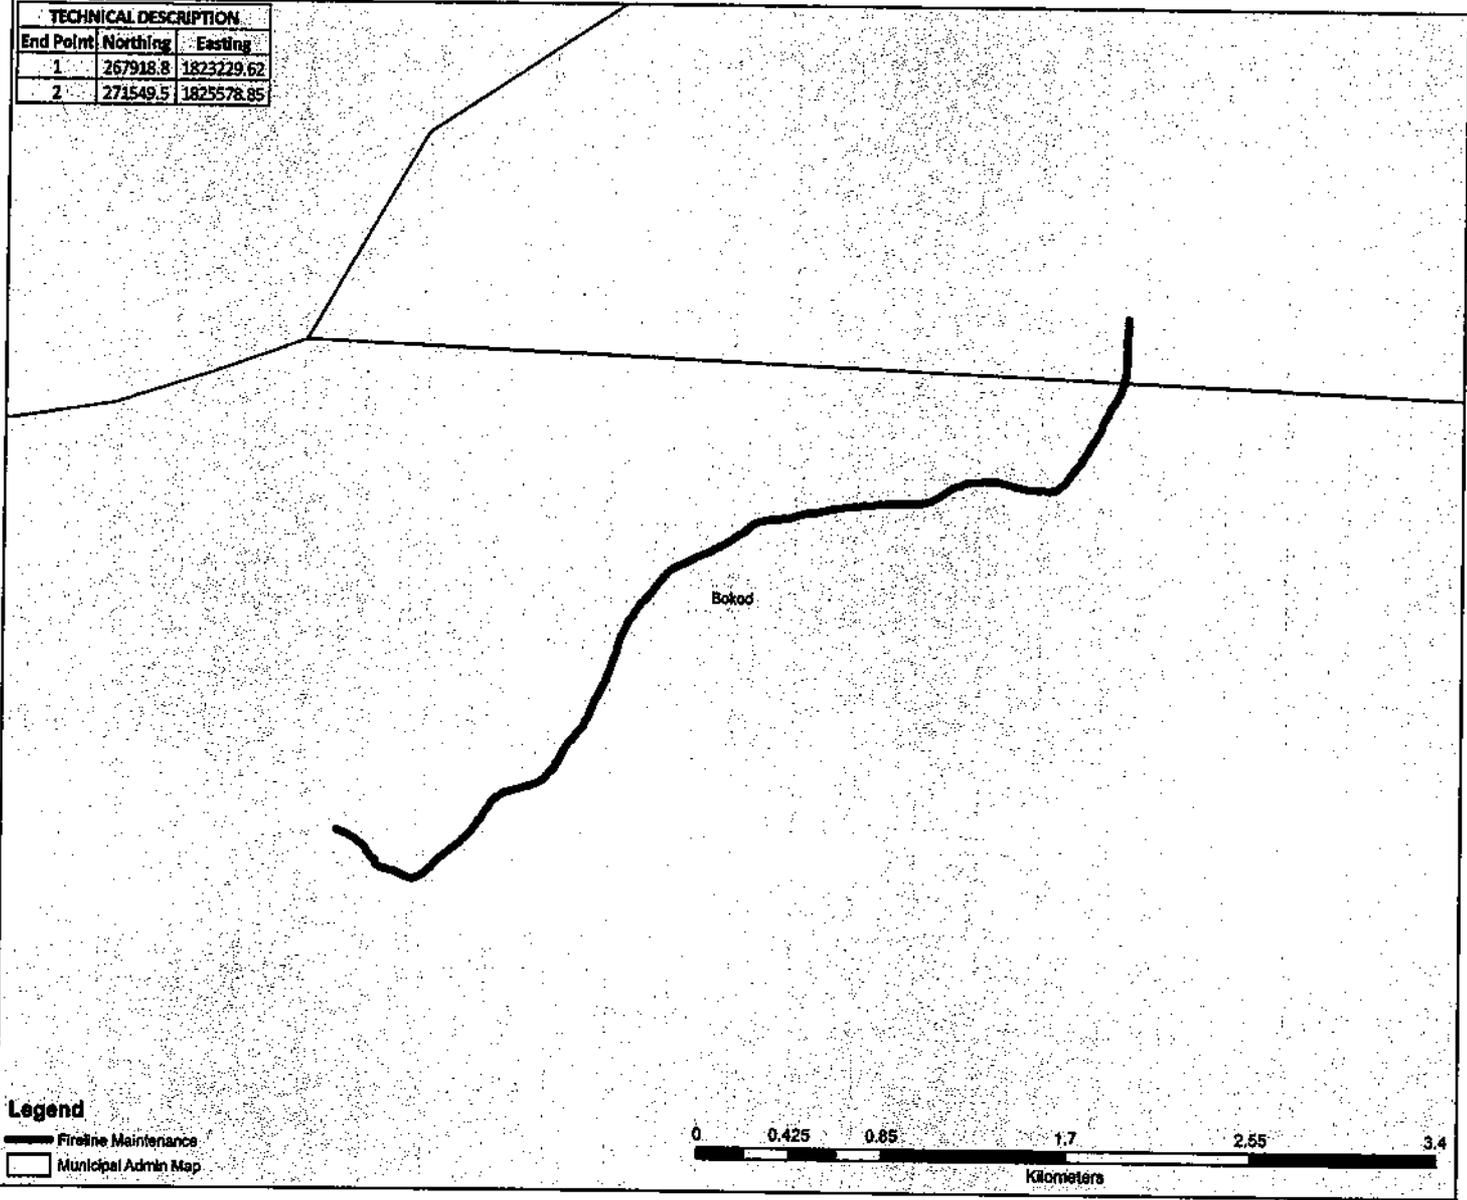

**LOCATION MAP**

Scale: 1:24,000  
 Map Projection:  
 Universal Traverse Mercator (UTM) Zone 51N  
 World Geodetic System (WGS) 1984

**FIRELINE MAINTENANCE- PLAN 9**

**PLAN**  
 AS PREPARED FOR  
 Upper Agno River Watershed Area Team  
 Watershed Management  
 National Power Corporation

**SITUATED IN THE:**  
 BARANGAY OF: POBLACION TO KARAO  
 MUN. / CITY OF: BOKOD  
 PROVINCE OF: BENGUET  
 ISLAND OF: LUZON  
 CONTAINING AN AREA OF: 4 LKM

**FINDINGS:**

1. VEGETATIVE COVER  
 ADEQUATELY FORESTED     INADEQUATELY STOCK  
 GRASSES/COGON             BARED/DENUDED

2. TOPO SITUATION  
 FLAT (0-18%)     ROLLING (19-30%)     STEEP (>30%)

3. OWNERSHIP  
 CLAN/FAMILY     ASSOCIATION     INDIVIDUAL

4. REP/CONTROL POINTS  
 BUFFER MONUMENT            NO. \_\_\_\_\_  
 PUBLIC LAND                    NO. \_\_\_\_\_  
 SUB-MONUMENT  
 CADASTRAL SURVEY  
 MONUMENT                    NO. \_\_\_\_\_  
 JUNCTION  
 \_\_\_\_\_ ROADS  
 \_\_\_\_\_ RIVERS

**LAND-USE SURVEY MAPPING**

**PREPARED BY:**  
  
**MHERWIN A. CIPRIANO**  
 Wat. Mgmt. Officer

**NOTED BY:**  
  
**BENJAMIN Z. KIMMAYONG**  
 Section Chief-UARWAT

# 53 LKM FIRELINE

## PROPOSED FIRELINE MAINTENANCE-PLAN 9

### Legend

-  Fireline Maintenance
-  Watershed Boundary

Google Earth

Image © 2022 Maxx Technologies  
Image analysis by Robert Yu

N

10 m

# POBLACION – KARAO (4 LKM)

## FIRELINE MAINTENANCE

Poblacion to Karao

### Legend

•• Fireline

Google Earth

Image © 2023 Google



4000 ft

# MAROOC – SAITAN (4 LKM)

## FIRELINE MAINTENANCE

Maro-oc to Saitan

### Legend

 Fireline

Google Earth

Image © 2022 Maxar Technologies

N

3000 ft

# BALOY – CAMISONG (4 LKM)

## FIRELINE MAINTENANCE

Baloy to Camisong


### Legend

• Fireline

Google Earth

Image © 2022 Maxar Technologies Ltd

4000 ft

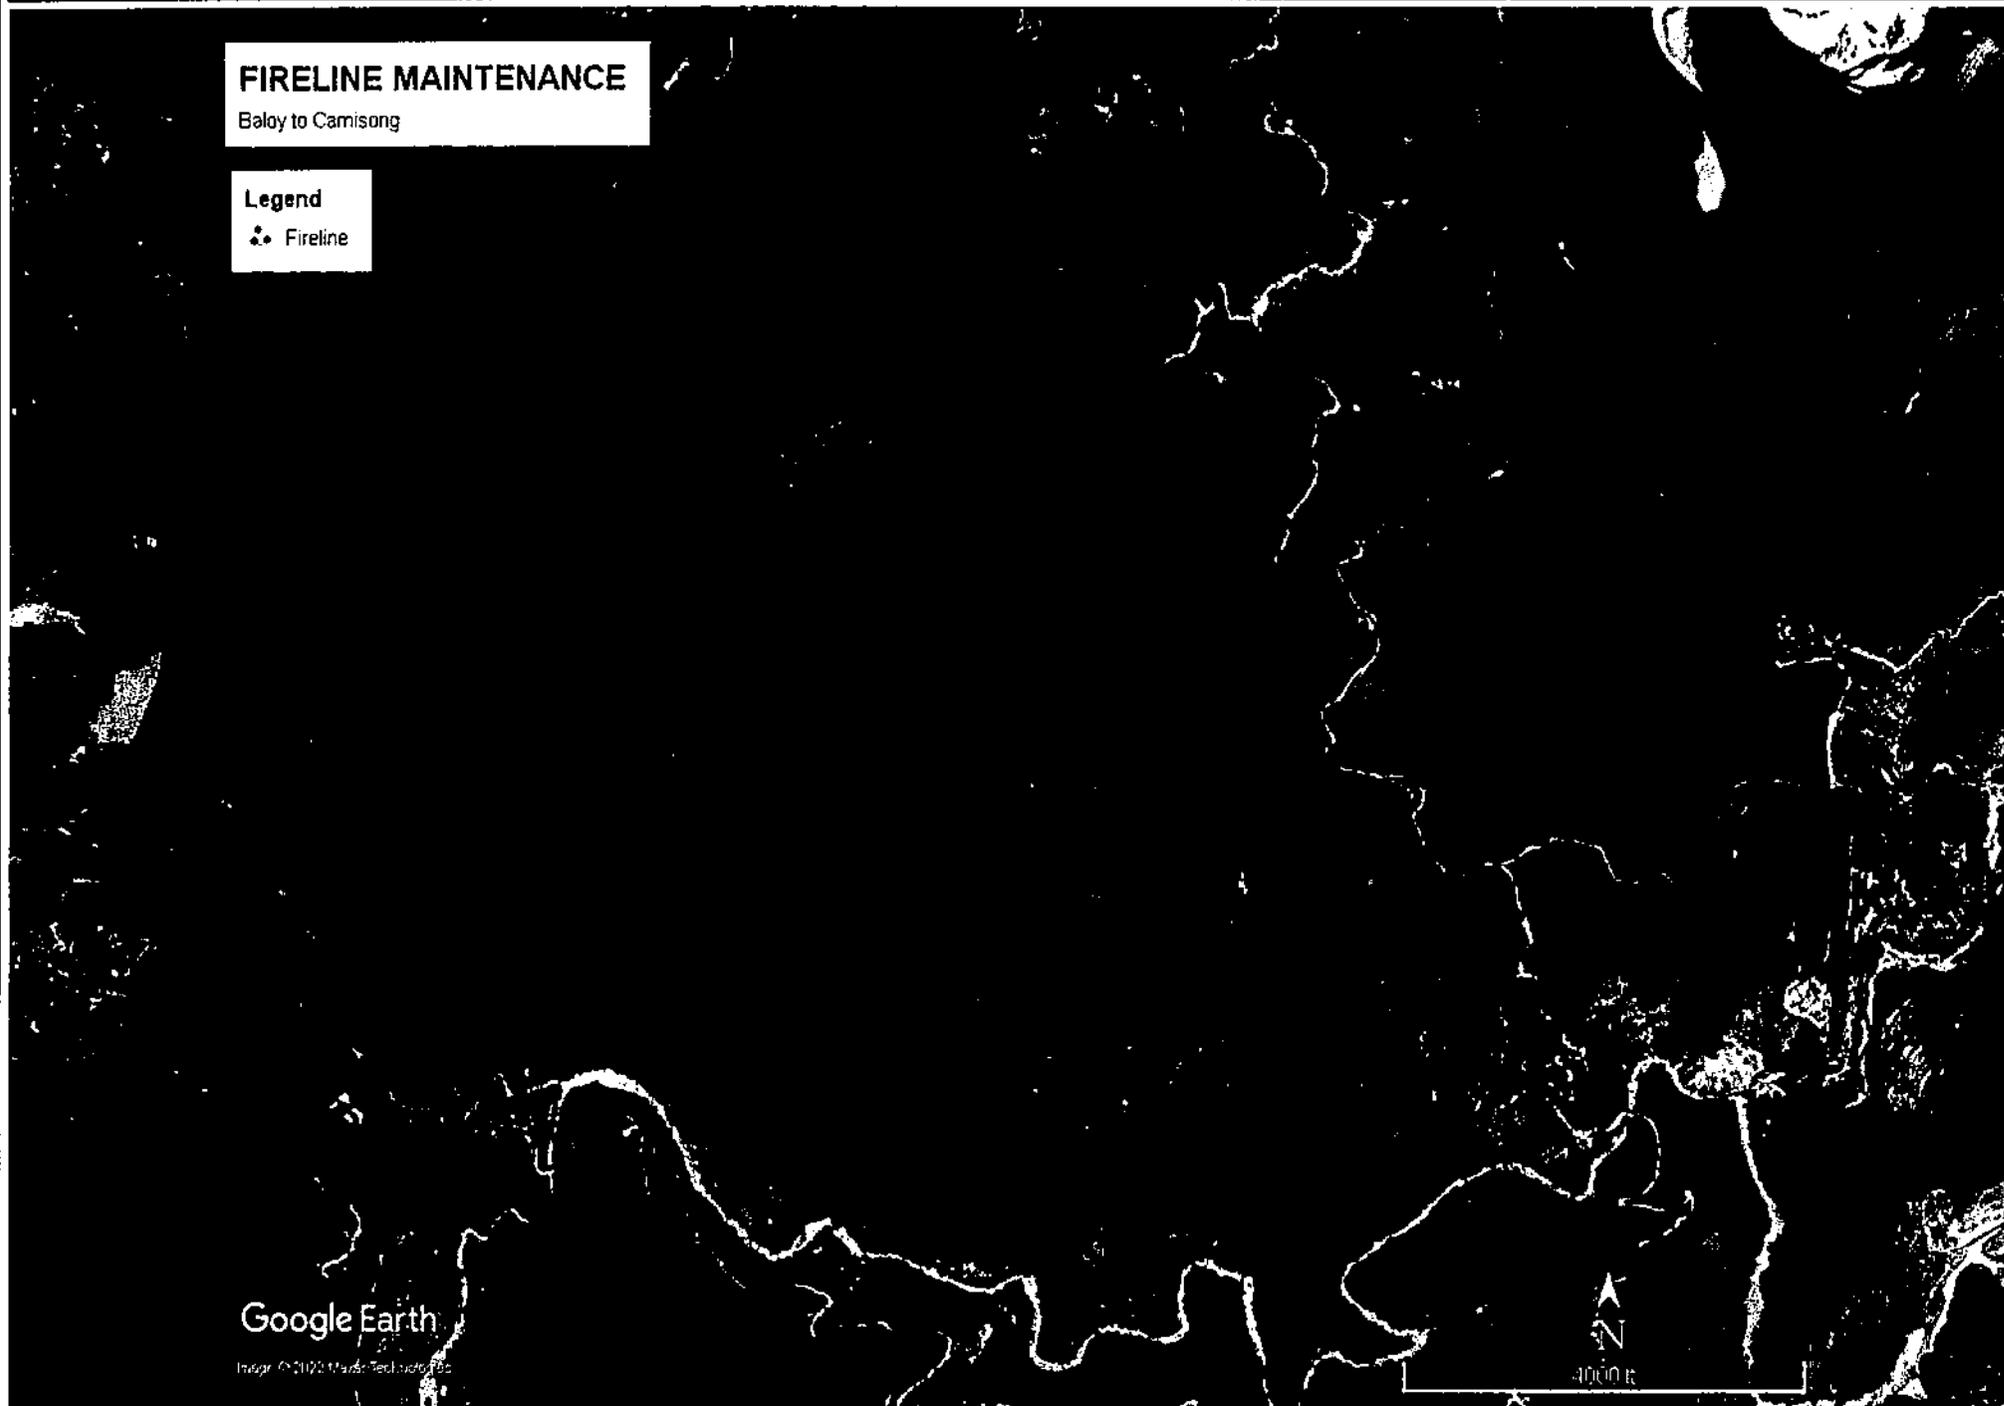

# COMODIAN – PALEW (4 LKM)

## FIRELINE MAINTENANCE

Comodian to Palew

### Legend

•• Fireline

Google Earth

© 2002 Google Technology



1 m

# ALAM-AM – SUGGLE (4 LKM)

## FIRELINE MAINTENANCE

Alam-am to Sugel

### Legend

•• Fireline

Google Earth

Map data ©2014 Google, Imagery ©2014 Google



N

4000 ft

# GEWENG - ADONOT (4 LKM)

## FIRELINE MAINTENANCE

Geweng to Adonot

### Legend

• Fireline

Google Earth

© 2002 Google Technology

1 km

# INIDIAN - DAMSHACK (4 LKM)

## FIRELINE MAINTENANCE

Indian to Damshack

### Legend


•• Fireline



4000 ft

Google Earth

© 2007 Google

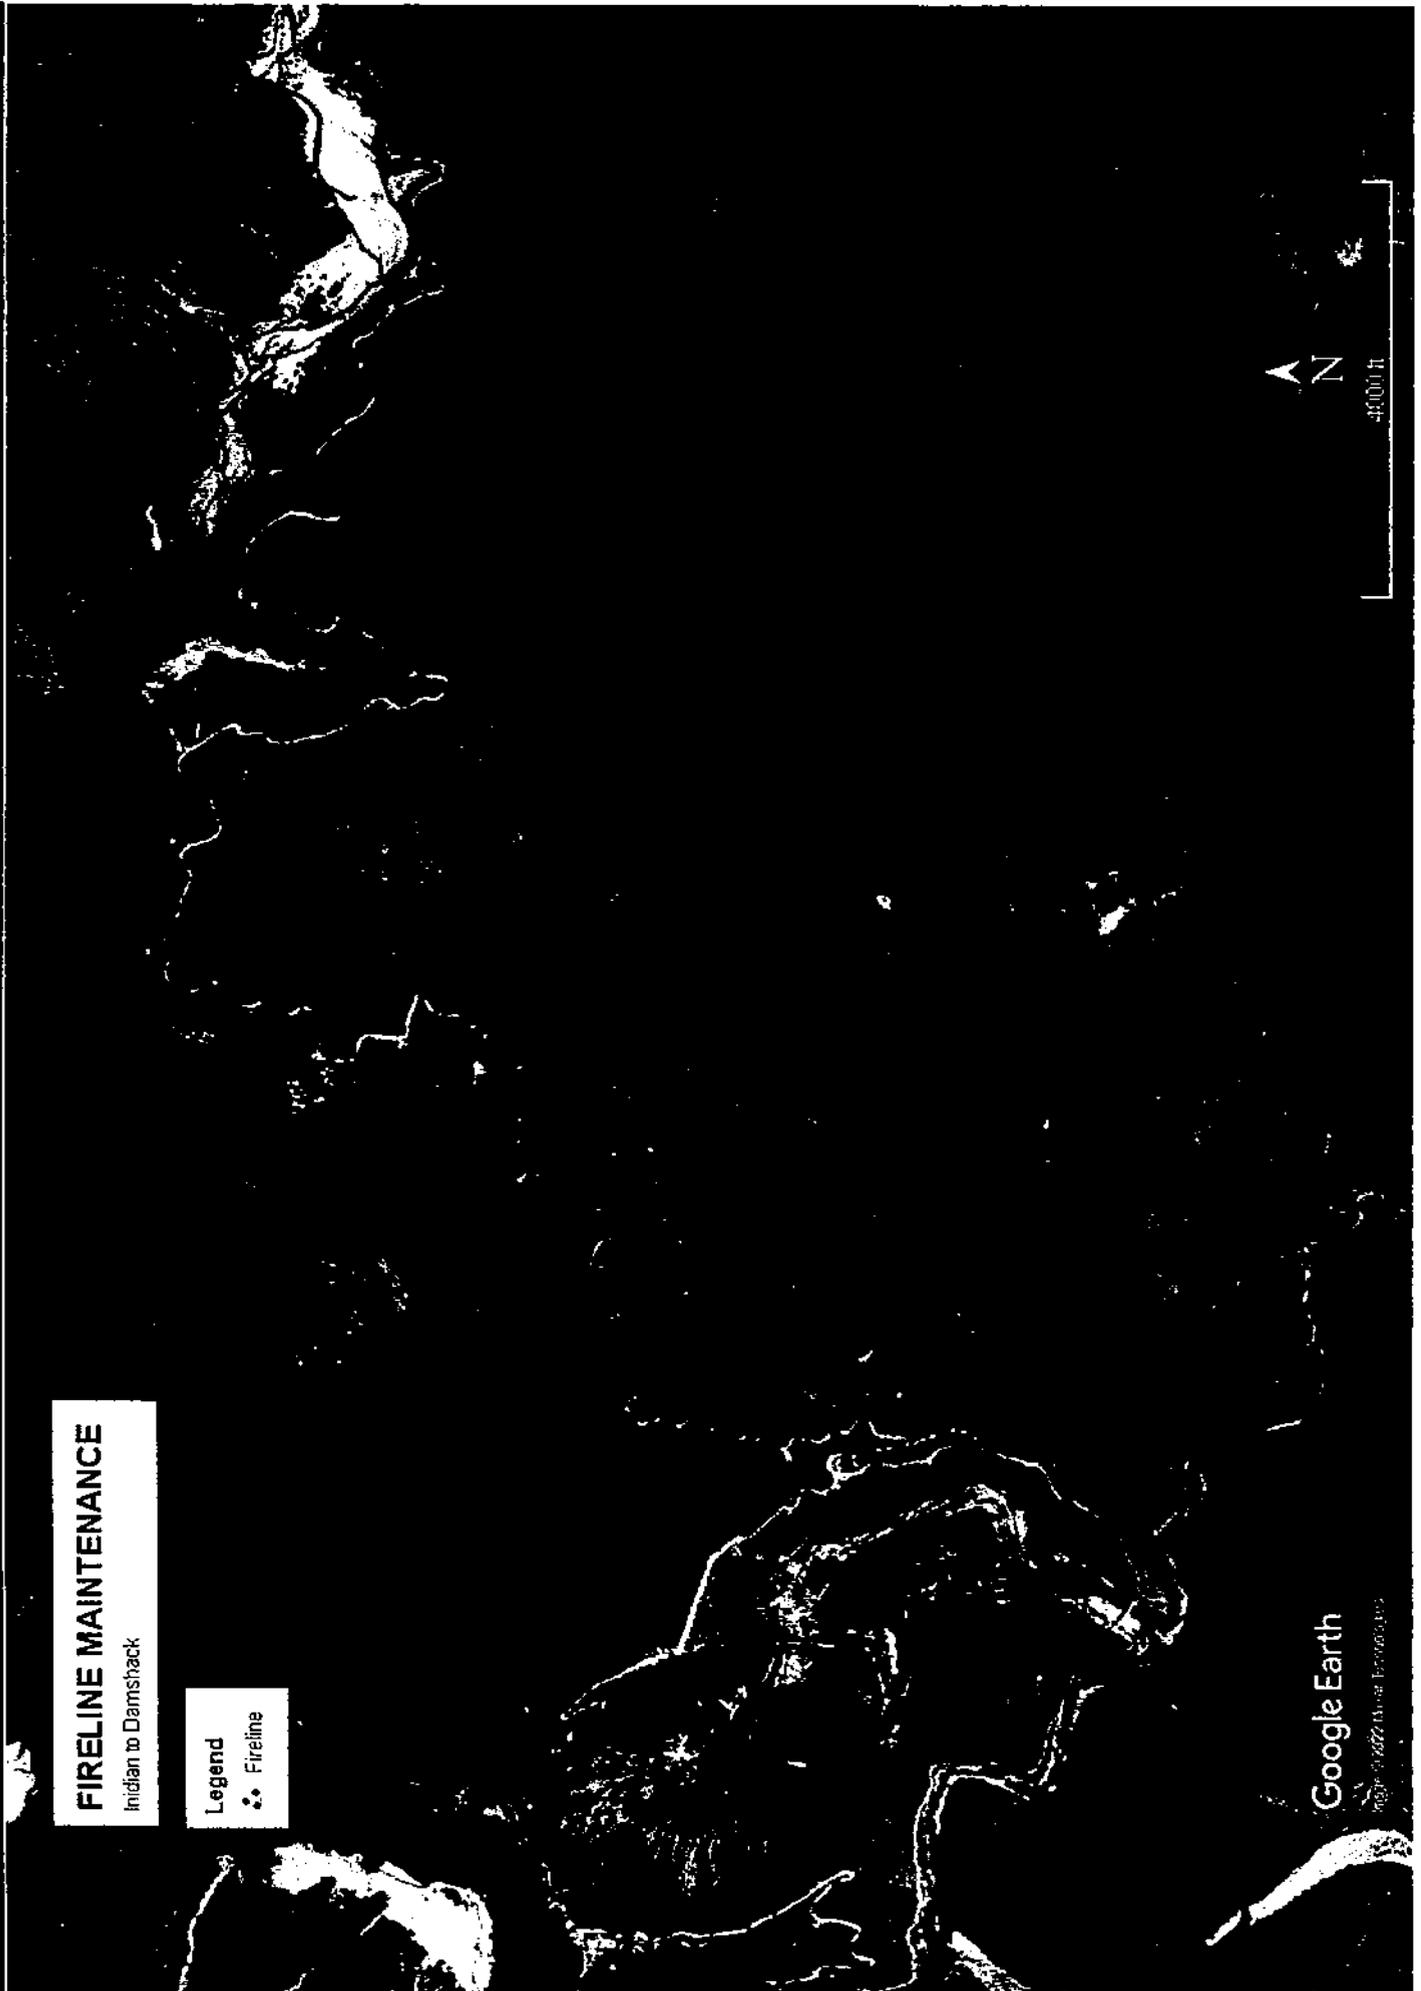

# BANGAO – KAWAL (4 LKM)

## FIRELINE MAINTENANCE

Kawal to Bangao

### Legend

••• Fireline

Google Earth

© 2002 Mapbox Technologies

4000 ft



# POBLACION - BAGDAN (3 LKM)

## FIRELINE MAINTENANCE

Poblacion to Bagdan

### Legend

•• Fireline

Google Earth

© 2005 Google

4000 ft



□



# HILLTOP – MT. PATOKTOK - DUTAC (5 LKM)

## FIRELINE MAINTENANCE

Hilltop- Mt. Patoktok-Dutac

### Legend


•• Fireline

Google Earth

© 2005 Google

N

4000 ft

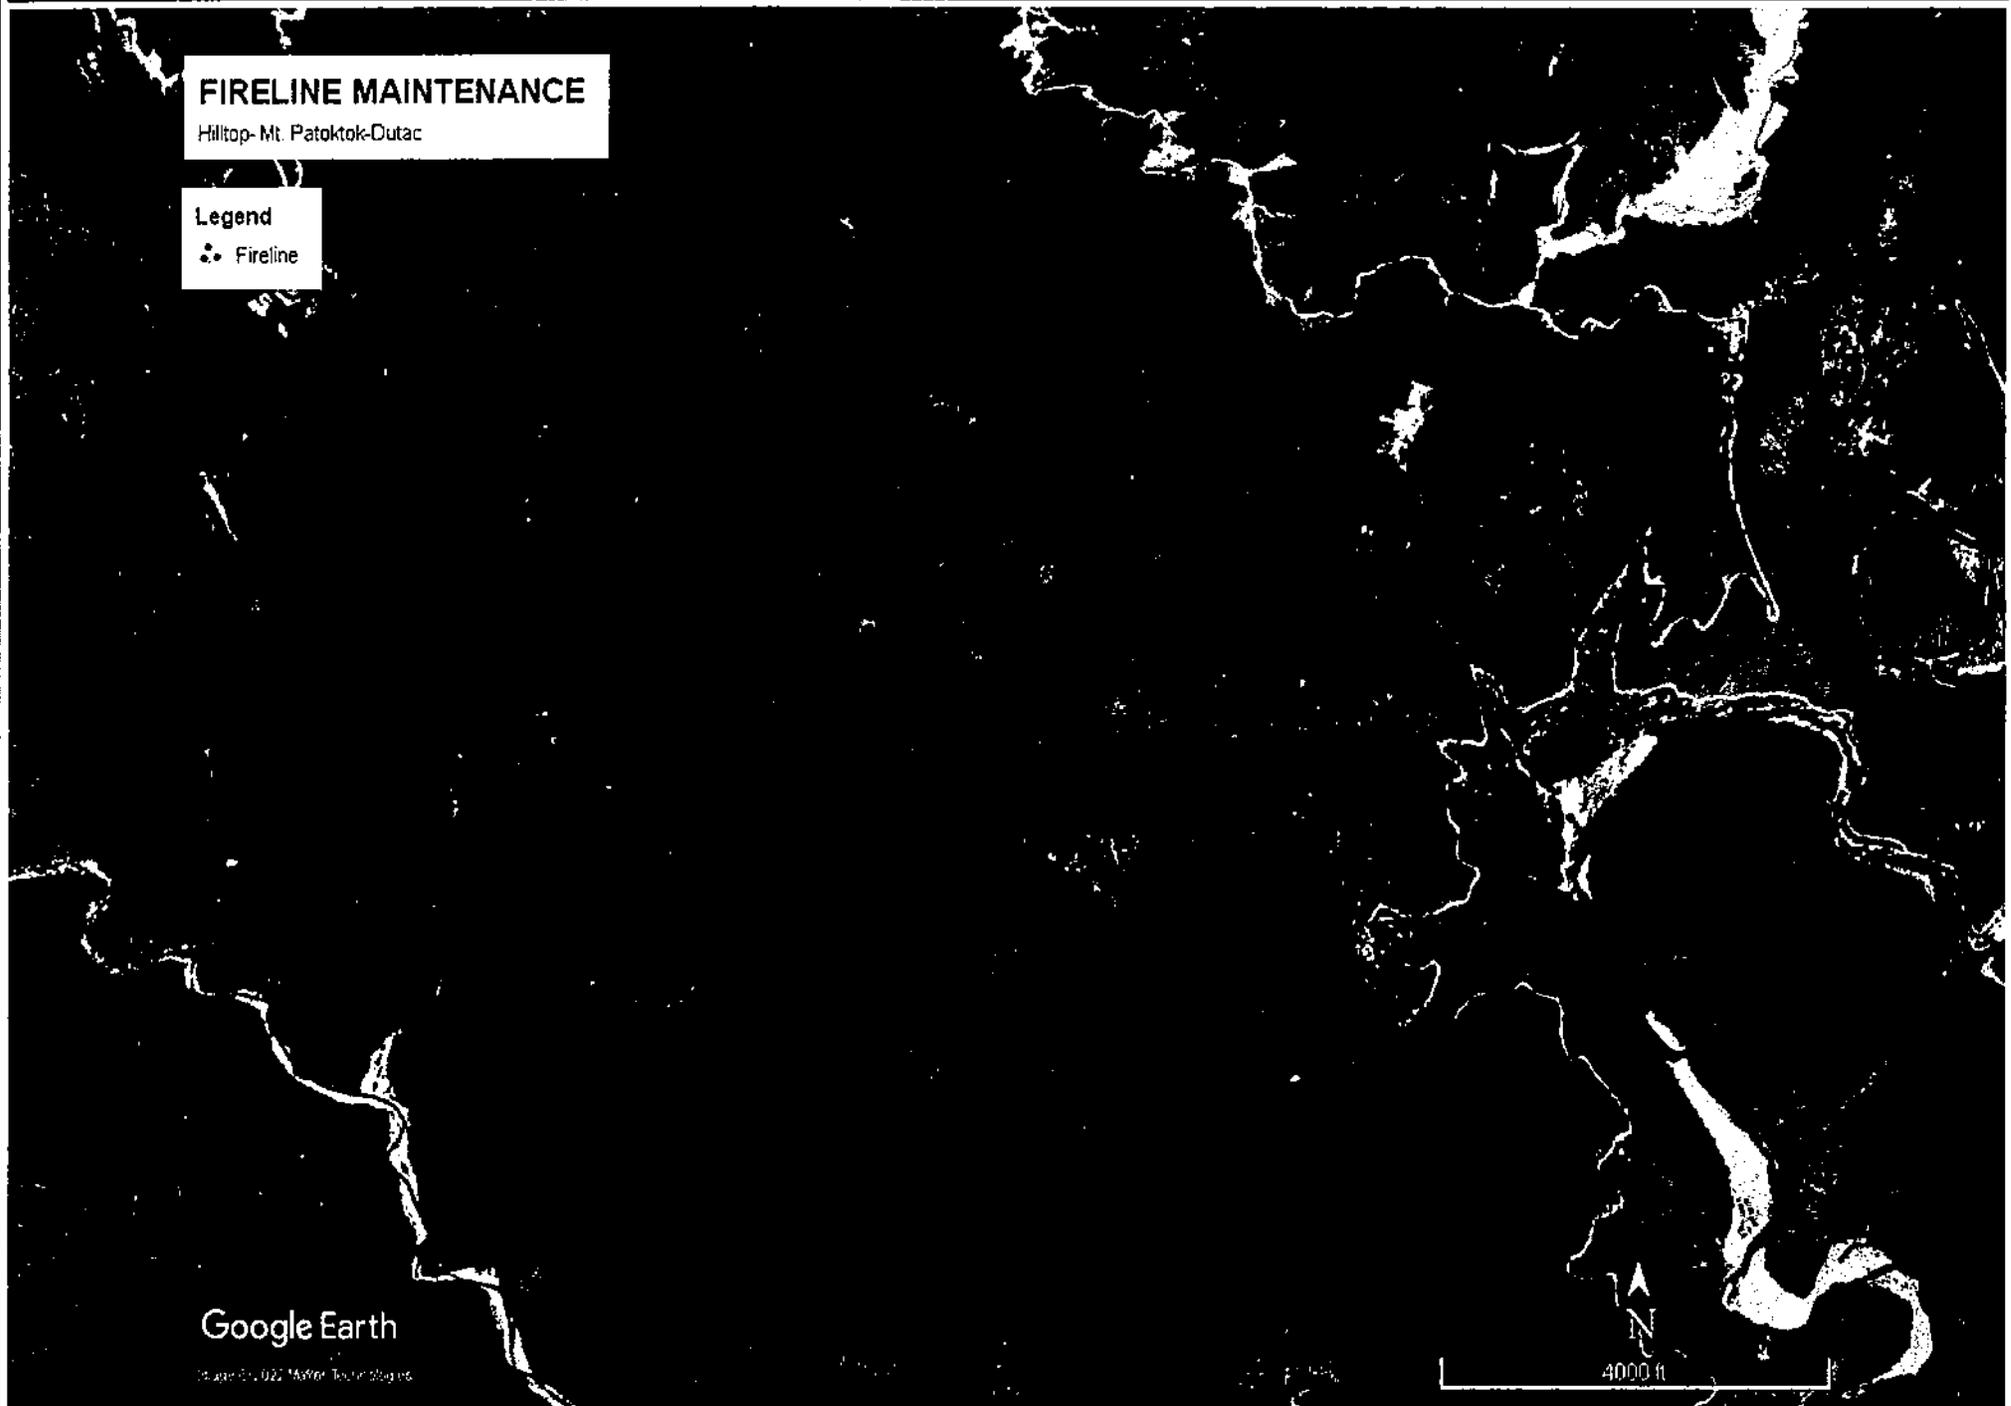

# BANGAO - GUSARAN (5 LKM)

## FIRELINE MAINTENANCE

Bangao to Gusaran

### Legend

•• Fireline

Google Earth

Image © 2002 Microsoft Corporation



2000 ft

# BACONG – MT. AMBOBONGAN (4 LKM)

## FIRELINE MAINTENANCE

Bacong to Mt. Ambobongan

### Legend

• Fireline

Google Earth

Image © 2002 Nasir Technologies



2000 ft

